

**Monthly Progress Report of Uttar Pradesh in the NGT Matter OA No. 673 of 2018
(In compliance to NGT order dated 24.09.2020)**

April 2023

I. Details of Sewage Treatment Plant in the State

Total Population of the state: 19.98 Crore as per census 2011.

a) Urban Population- 4.44 Crore in Year 2011

b) Rural Population- 15.54 Crore in Year 2011

Total Estimated Sewage Generation (MLD): 5500 MLD

a) Total existing treatment capacity of 122 STPs :- 3860 MLD (Annexure-1)

b) Existing 122 STPs utilization capacity :- 2986 MLD

c) Current Gap:- 1640 MLD

d) 55 STPs under construction :- 1082 MLD (Timeline Dec. 2024) (Annexure-2)

e) 12 STPs under tendering :- 776 MLD (Timeline June 2025) (Annexure-3)

f) 317 STPs proposed :- 1593 MLD (Timeline Dec. 2025) (Annexure-4)

Performance of Sewage Treatment Plant(As per UPPCB March 2023 Analysis Reports)

S.No	STPs in UP	Number
1	Total Installed STP	122 (Total Capacity- 3860 MLD)
2	Operational STP	110 (Utilized Capacity: 2986 MLD)
3	STP Achieving norms (in terms of GP+FC)	81
	STP Not Achieving norms (in terms of GP + FC)	24
4	STP Achieving norms (in terms of GP)	105
	STP Not Achieving norms (in terms of GP)	5

The standards as per MOEF&CC Notification dated 13.10.2017, titled "Applicable Effluent Discharge Standards for STPs" are as follows:

For State Capital: pH-6.5-9.0; BOD - <20 mg/l; TSS- <50 mg/l & FC- <1000 MPN/100 ml

Other than State Capital: pH-6.5-9.0; BOD - <30 mg/l; TSS- <100 mg/l & FC- <1000 MPN/100 ml

II. Details of Industrial Pollution:

Status of GPI Industries inspected during 2021-22

Total Industries Inspected	Non-Compliant units
1377	247

Note: GPI Industries inspection for Year 2022-23 is in progress.

Status of Common Effluent Treatment Plants (CETPs)

- Number of existing CETP :- 07 (Annexure-5)
- Capacity of CETP :- 58.55 MLD
- No. of Upgradation/ under construction CETP :- 05
- Capacity of under construction CETP:- 32.4 MLD

Performance of Common Effluent Treatment Plant :-

S.No	CETP in Uttar Pradesh	Number
1	Total Installed CETP	7
2	Operational CETP	7
	CETP Achieving Norms	6
	CETP Not Achieving Norms	1

Detail of under construction/proposed CETP

S. No	Name of District	Capacity (MLD)	Agency/ Project	Timeline/ Date of Commissioning	Remark
1	Jajmau, Kanpur Nagar	20	JATETA	Aug, 2023	-
2	Bhadohi	1	-	-	-
3	SEZ, Moradabad	2.4	UPSIDA	-	-
4	Growth Centre, Jainpur, Kanpur Dehat	2	UPSIDA	March, 2023	-
5	GIDA, Gorakhpur	7	Namami Gange & Urban Development	July, 2024	ToR for Environmental Cleanrance issued by SIEAA. EIA Study pending at PP

Remark :- Other than mentioned above a CETP of 75 KLD is proposed at Lakahnpur , Agra for 30 small scale electroplating units on Zero Liquid Discharge (ZLD)technology installed by Lakhanpur Small Scale Electroplating Ind. Association (Timeline for operation is July 2023).

III. Solid Waste Management:


Total Population of the state: 19.98 Crore as per census 2011.

- a) Urban Population- 4.44 Crore in Year 2011
- b) Rural Population- 15.54 Crore in Year 2011

(A). Solid Waste Management (Urban):


- Total number of Urban Local Bodies :- 734
- Urban Population- 4.44 Crore in Year 2011
- Current Municipal Solid Waste Generation- **14710 TPD**
 - a) Total existing treatment capacity :- 10117 TPD (Annexure-6)
 - b) Current GAP:- 4593 TPD
 - c) Plants under construction :- 7526 TPD (Timeline Dec. 2023) (Annexure-7)
 - d) Proposed Treatment Facilities :- 6280 TPD (Timeline March 2025)(Annexure-8)
 - e) Segregation at source :- 12504 TPD

Solid Waste Management (Urban)

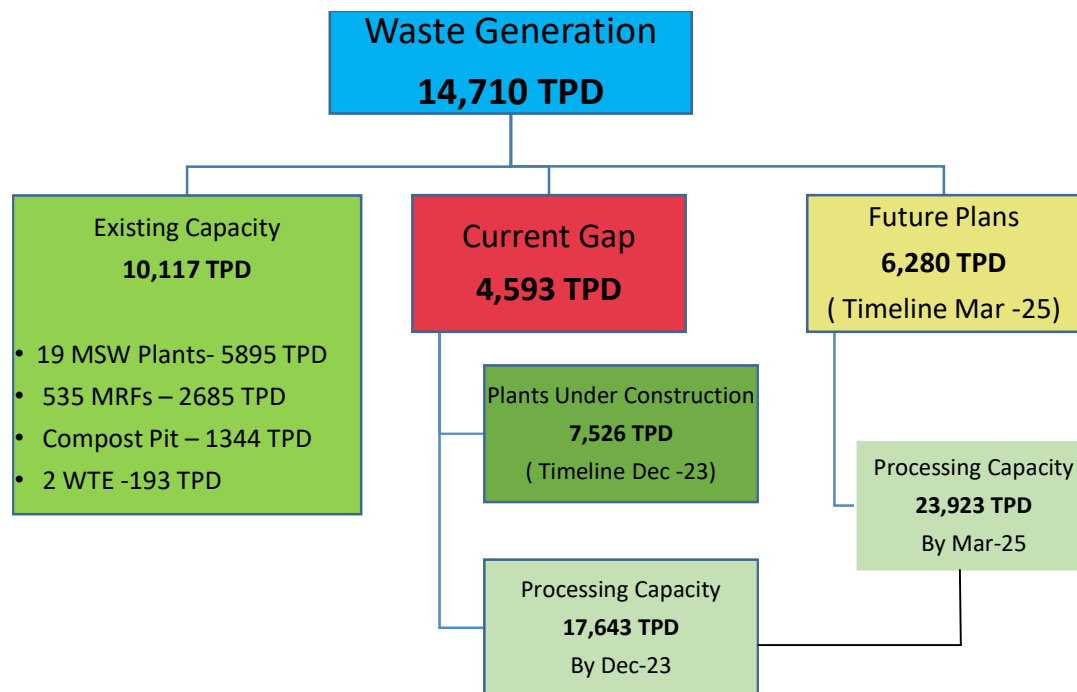

(B). Solid Waste Management (Rural):

- Rural Population- 15.54 Crore in Year 2011
- Current Municipal Solid Waste Generation- **11959 TPD**
 - a) Total existing treatment capacity :- 3000 TPD
 - b) Current GAP:-8959 TPD
 - c) Proposed Treatment Facilities :- 8959 TPD (Timeline March 2025)

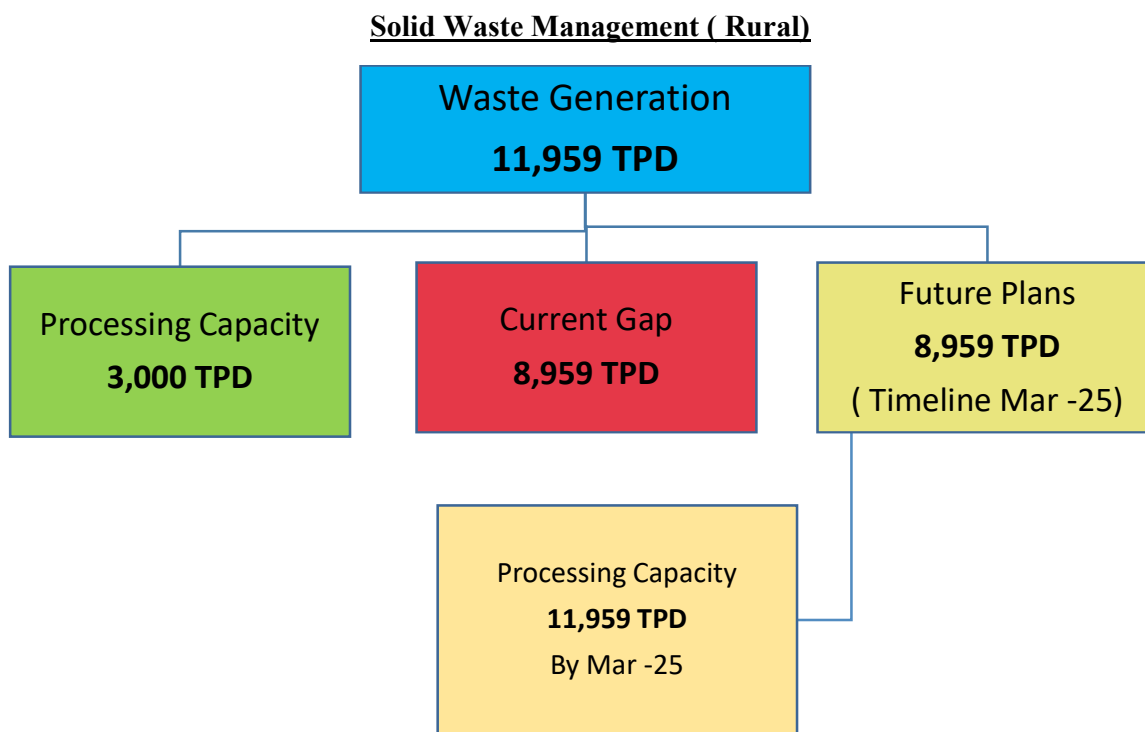


(C) Details of legacy waste in the State:-

- a) Total legacy waste dump sites :- 75 (Annexure-9)
- b) Total area of legacy waste dump sites:-627 acre
- c) Estimated quantity :- 91 Lac Ton
- d) Remediated waste :- 58 Lac Ton
- e) Ongoing Remediation:- 33 Lac Ton(Timeline March 2024)
- f) **No. and area (in acres) of legacy waste within 1.0 km buffer of both side of the rivers:-**There is no legacy waste site situated within 1 KM of the banks of rivers.

IV. Construction & Demolition Waste :

- Current C&D Waste Generation :- **1471 TPD**
 - a) Total processing capacity :- 1205 TPD
 - b) Current GAP:- 266 TPD
 - c) Plants under construction :- 300 TPD (Timeline Sep. 2023)
 - d) Proposed Treatment Facilities :- 970 TPD (Timeline March 2024)

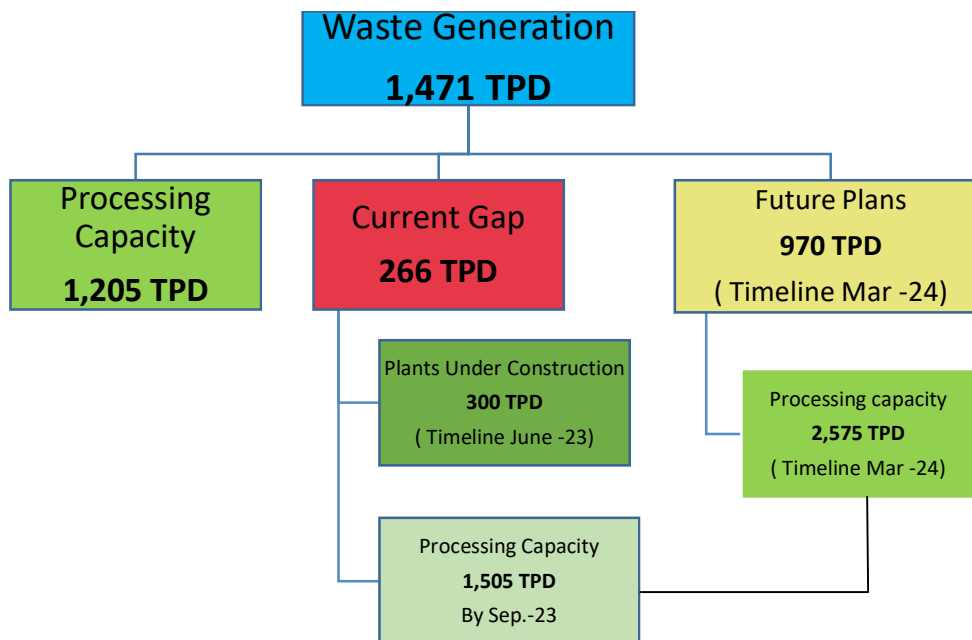

a) Districtwise detail of Operational C& D Waste Processing Facilities:-

S.No	Operational	Capacity
1.	Agra	05 TPD
2.	Varanasi	200 TPD
3.	Prayagraj	100 TPD
4.	Ghaziabad	400 TPD
5.	Noida	400 TPD
6.	Lucknow	100 TPD
Total		1205 TPD

b)Under Construction C& D Waste Processing Facilities:-

S.No.	Under Construction	Capacity	Timeline
1.	Kanpur(75% work completed)	100 TPD	June 2023
2.	Lucknow (20% work completed)	200 TPD	Sep. 2023
Total		300 TPD	

c)Proposed C& D Waste Processing Facilities:-

S.No.	Proposed	Capacity	Timeline
1.	Aligarh	100 TPD	31.03.2024
2.	Meerut	200 TPD	31.03.2024
3.	Moradabad	100 TPD	31.03.2024
4.	Gorakhpur	50 TPD	31.03.2024
5.	Firozabad	50 TPD	31.03.2024
6.	Jhansi	50 TPD	31.03.2024
7.	Ayodhya	20 TPD	31.03.2024
8.	Mathura	50 TPD	31.03.2024
9.	Kanpur	200 TPD	31.03.2024
10.	Agra	150 TPD	31.03.2024
Total		970 TPD	

V. Bio-medical Waste Management:

- Total Bio-medical generation: 71264.2 Kg/day
- No. of Hospitals and Health Care Facilities: 37,927
- Status of Treatment Facility/ CBMWTF: 22

VI. Plastic Waste Management:

- Total Plastic Waste generation: 1030 TPD
- Uttar Pradesh has potential for disposal of Plastic Waste of 2360TPD

S.No.	Mode of Disposal	Disposal Capacity
1.	Recycling Facilities (82 Number)	1908.5 TPD
2.	Co-processing Facilities-01 (M/s Ultratech Cement, Sonebhadra)	150 TPD
3.	Waste to Oil -03	33.1 TPD
4.	Waste to Energy-03	268.97
Total recycling & disposal infrastructure in UP- 2360.06 TPD		

VII. Details of Nodal Officer appointed by Chief Secretary in the State/UT: Three tier monitoring mechanism developed and functional.

VIII. Latest water quality of polluted river, its tributaries, drains with flow details and ground water quality in the catchment of polluted river: Latest water quality status of polluted river stretches is available at link <http://www.uppcb.com/data-of-year-2022.htm>.

IX. Demarcation of Floodplain and removal of illegal encroachments:

- 14446 pillars have been placed against 15293 pillars for demarcation of floodplain zone of River Ganga from Kannauj to Unnao.
- Flood Plain Zones for Rivers Hindon, Yamuna, Varuna, Gomti, Kali east, Ramganga, Betwa, Ghaghra, Rapti, Sai, Saryu has been decided.

X. Maintaining minimum e-flow of river:

- E-flow for Kannauj-Unnao maintained as per directions of CWC.
- E-flow in Rivers Ghaghra, Rapti, Ramganga, Saryu, Betwa has been decided.
- E-flow for River Yamuna and Ganga (Unnao-UP Border) yet to be decided.
- Rivers Sai, Gomti, Varuna, Hindon, Kali east are non-perennial rivers, e-flow cannot be maintained

XI. Plantation activities along the rivers:

- Total **1,63,80,540** (One Crore Sixty Three Lakh Eighty Thousand five hundred and forty saplings have been planted along 14 polluted river stretches in the year 2021-22.
- Total **2,32,88,553** (Two Crore Thirty Two Lakh Eighty Eight Thousand Five Hundred and Fifty Three saplings have been planted along 14 polluted river stretches in the year 2022-23.

XII. Reutilization of Treated Sewage from STP:

- a) 8 MLD treated water from Trans - Yamuna –I and II STPs at Mathura is supplied to IOCL, Mathura.
- b) Treated sewage and sludge from the STP is auctioned to farmers, used in land filling and as manure, disposed in Nagar Palika land, for construction activity and in Horticulture (Miyawaki).
- c) **Future Plan: -**

S.No.	Re-utilization of treated sewage	Timeline
1.	Treated water from Bingawan STP (210 MLD) to Panki Thermal Power Plant (approx. 40 MLD)	June, 2023
2.	20 MLD treated water from Trans - Yamuna –I and II STPs at Mathura is to be supplied to IOCL, Mathura	December, 2023
3.	Treated water from Shahjahanpur STP (45 MLD) to Rosa TPS (approx. 40 MLD)	June, 2025
4.	Treated water from Aligarh STP (45 MLD) to Harduaganj TPS (approx. 30 MLD)	July, 2025
5.	Treated water from Naini, Prayagraj STP (80 MLD) to Bara TPS (approx. 55 MLD)	December, 2025
6.	Treated water from Bulandshahar STP (40 MLD) to Rosa TPS (approx. 20 MLD)	July, 2025

XIII. Model River being adopted by the State & Action Proposed for achieving the bathing quality standards: Not adopted yet.

Annexure-1

Details of existing STPs in Uttar Pradesh (April 2023)

S.No.	Name of Town/ District	Name of STP	Year of Commissioning	Design Technology	Capacity of STP (MLD)	Primary Agency Maintaining the STP	Compliance Status as per MOEFCC notification dated 13.10.2017
1	Agra	Bichhpuri	2012	UASB	40	UPJN (Urban)	Achieving
2	Agra	Bichhpuri - 2	2013	SBR	36	ADA	Achieving
3	Agra	Dandupura	2013	UASB	78	UPJN (Urban)	Achieving
4	Agra	Dandupura - 2	2013	UASB	24	UPJN (Urban)	Achieving
5	Agra	Devri Road	2011	UASB	12	UPJN (Urban)	Achieving
6	Agra	Jaganpur	2010	UASB	14	UPJN (Urban)	Achieving
7	Agra	Kalandi Bihar	2013	UASB	4.5	ADA	Achieving
8	Agra	Naglaburhi	2000	WSP	2.25	UPJN (Urban)	Achieving
9	Agra	Pilkhar	2000	WSP	10	UPJN (Urban)	Achieving
10	Anupshahar	Aahar Road	2001	WSP	0.81	UPJN (Urban)	Not Achieving
11	Anupshahar	Shivanand Asharam	2001	WSP	1.76	UPJN (Urban)	Not Achieving
12	Anupshahar	Anupshahar (NGRBA) Zone-A	2018	UASB	1.5	UPJN (Rural)	Achieving
13	Anupshahar	Anupshahar Zone B	2018	MBBR	1	UPJN (Rural)	Achieving
14	Ayodhya	Ramghat Ayodhya	2014	UASB	12	UPJN (Urban)	Achieving
15	Baghpat	Baghpat	2022	SBR	14	UPJN (Rural)	Achieving
16	Bijnour	Bijnour	2018	UASB	24	UPJN (Urban)	Achieving
17	Bulandshahar	Bulandshahar	2022	SBR	40	UPJN (Urban)	Achieving
18	Chitrakoot	Near Viklang Kendra	2016	Oxidation Pond	3.42	NPP	Not Achieving
19	Etah	Manpur	2021	SBR	24	UPJN (Urban)	Achieving
20	Etawah	Karanpur	2000	WSP	10.45	UPJN (Rural)	Achieving
21	Etawah	Umren	2013	SBR	13.45	UPJN (Rural)	Achieving
22	Etawah	Etawah	2022	SBR	21	UPJN (Rural)	Achieving
23	Fatehgarh	Fatehgarh	1993	Oxidation Pond	2.7	UPJN (Urban)	Not Achieving
24	Firozabad	Firozabad	2012	UASB	3	NPP	Achieving
25	Firozabad	Mohammadpur	2021	ASP+BNR	67	UPJN (Urban)	Achieving
26	Garhmukteshwar	Garhmukteshwar-I	2018	UASB	6	UPJN (Rural)	Achieving
27	Garhmukteshwar	Garhmukteshwar-II	2018	UASB	3	UPJN (Rural)	Achieving
28	Ghaziabad	Bapudham	2018	UASB	56	GDA	Achieving
29	Ghaziabad	Dudaheda	2013	SBR	56	UPJN (Urban)	Achieving
30	Ghaziabad	Dudaheda - 3	1998	UASB	70	UPJN (Urban)	Not Achieving
31	Ghaziabad	Govindpuram	2012	UASB	56	GDA	Achieving
32	Ghaziabad	Indirapuram	2013	SBR	74	UPJN (Urban)	Achieving
33	Ghaziabad	Indirapuram - 2	1998	UASB	56	UPJN (Urban)	Achieving
34	Ghaziabad	Indirapuram 3	2012	UASB	56	GDA	Not Achieving
35	Ghaziabad	Morti Rajendra Nagar Extension	2011	SBR	56	GDA	Achieving

36	Gorakhpur	Mahadev Jharkhandi	2010	SBR	15	UPJN (Urban)	Achieving
37	Gorakhpur	Ramgarhtal	2015	SBR	30	UPJN (Urban)	Achieving
38	Greater Noida	Badalpur	2013	SBR	2	Greater Noida	Achieving
39	Greater Noida	Ecotech 2nd	2018	SBR	15	Greater Noida	Achieving
40	Greater Noida	Ecotech 3rd	2018	SBR	20	Greater Noida	Achieving
41	Greater Noida	Kasna	2013	SBR	137	Greater Noida	Achieving
42	Hapur	Hapur	2022	SBR	30	UPJN (Urban)	Achieving
43	Jhansi	Laxmi Tal	2021	SBR	26	UPJN (Urban)	Achieving
44	Kannauj	Kannauj (State/ NGRBA)	2015	SBR	13	UPJN (Urban)	Achieving
45	Kanpur	Bingaon	2015	UASB	210	UPJN (Rural)	Not Achieving
46	Kanpur	Jajmau	1994	UASB	36	UPJN (Urban)	Not Achieving
47	Kanpur	Jajmau - 2	1999	ASP	130	UPJN (Rural)	Not Achieving
48	Kanpur	Jajmau - 3	1989	UASB	5	UPJN (Urban)	Not Achieving
49	Kanpur	Kanpur (JNNURM)	2016	UASB	43	UPJN (Rural)	Not Achieving
50	Kanpur	Sajari	2016	ASP	42	UPJN (Rural)	Achieving
51	Kanpur	Baniyapur	2018	SBR	15	UPJN (Urban)	-
52	Kasganj	Kasganj	2022	SBR	15	UPJN (Rural)	Achieving
53	Loni	Loni	2013	MBBR	30	UPJN (Urban)	Achieving
54	Loni	Tronica City	2020	MBBR	5	UPSIDA	Achieving
55	Lucknow	Awas Vikas STP	2017	SBR	37.5	Awas Vikas	Achieving
56	Lucknow	Bharwara	2016	UASB	345	UPJN (Urban)	Not Achieving
57	Lucknow	Daulatganj	2003	FAB	42	UPJN (Urban)	Achieving
58	Lucknow	Daulatganj - 2	2009	FAB	14	UPJN (Urban)	Achieving
59	Lucknow	Jalkal	2010	SBR	6.5	Jalkal	Achieving
60	Mainpuri	Powerhouse Road	2014	UASB	23	UPJN (Urban)	Achieving
61	Mathura	Mosani	2000	WSP	6.8	UPJN (Rural)	Achieving
62	Mathura	Trans Yamuna	2016	UASB	16	UPJN (Rural)	Achieving
63	Mathura	Trans Yamuna (Gowardhan)	2010	WSP	2.76	NPP	Not Achieving
64	Mathura	Trans Yamuna - 2	2000	WSP	14.5	UPJN (Rural)	Achieving
65	Mathura	Masani	2021	SBR	30	UPJN (Rural)	Achieving
66	Meerut	Ganga Nagar	2011	SBR	10	MDA	Not Achieving
67	Meerut	Lohia Nagar	2010	ASP	10	MDA	Not Achieving
68	Meerut	Major Dhyan Chand	2012	ASP	7	MDA	Not Achieving
69	Meerut	Modipuram Tiraha	2016	ASP	5	MDA	Not Achieving
70	Meerut	Pallavpuram	2012	ASP	7	MDA	Not Achieving
71	Meerut	Pallavpuram - 2	2008	ASP	11	MDA	Not Achieving
72	Meerut	Pandav Nagar	2008	ASP	3	MDA	Not Achieving
73	Meerut	Rakshapuram	2011	ASP	6	MDA	Not Achieving
74	Meerut	Saardapuri Phase 2	2011	SBR	6	MDA	Not Achieving
75	Meerut	Sainik Vihar	2017	UASB	6	MDA	Not Achieving

76	Meerut	Sharda Puri Phase-I	2011	ASP	6	MDA	Not Achieving
77	Meerut	Shatabdi Nagar	2010	ASP	15	MDA	Not Achieving
78	Meerut	Ved Vyaspur	2010	ASP	15	MDA	Not Achieving
79	Meerut	Village Kamalpur	2016	ASP	72	UPJN (Urban)	Achieving
80	Mirzapur	Pucca pokhra	1993	UASB	14	UPJN (Rural)	Not Achieving
81	Mirzapur	Vindhyachal	2022	WSP	7	UPJN (Urban)	Achieving
82	Modinagar	Modinagar	2022	SBR	20	UPJN (Urban)	Achieving
83	Moradabad	Moradabad (NGRBA)	2018	UASB	58	UPJN (Rural)	Achieving
84	Muzaffar nagar	Kidwai nagar	2001	WSP	32.5	UPJN (Urban)	Not Achieving
85	Narora	Narora (NGRBA)	2019	UASB	4	UPJN (Rural)	Achieving
86	Narora	Narora Atomic Power Plant	2010	ASP	2.25	Narora Atomic Power Plant	Achieving
87	Noida	Sector-123	2009	SBR	35	Noida	Achieving
88	Noida	Sector-168	2009	SBR	50	Noida	Achieving
89	Noida	Sector-50	2009	SBR	25	Noida	Achieving
90	Noida	Sector-50-2	2013	SBR	34	Noida	Achieving
91	Noida	Sector-54-2	2009	SBR	33	Noida	Achieving
92	Noida	Sector-54-3	2013	SBR	54	Noida	Achieving
93	Noida	STP 168	2022	SBR	100	Noida	Achieving
94	Pilkhua	Pilkhua	2011	ASP	3	UPJN (Urban)	Achieving
95	Prayagraj	Kodra	2013	HRBF	25	UPJN (Rural)	Achieving
96	Prayagraj	Naini	1999	ASP	60	UPJN (Rural)	Achieving
97	Prayagraj	Naini - 2	2013	ASP	20	UPJN (Rural)	Achieving
98	Prayagraj	Numayadih	2013	HRBF	50	UPJN (Rural)	Achieving
99	Prayagraj	Ponghat	2013	HRBF	10	UPJN (Rural)	Achieving
100	Prayagraj	Rajapur	2013	UASB	60	UPJN (Rural)	Achieving
101	Prayagraj	Salori - 2	2016	SBR	14	UPJN (Urban)	Achieving
102	Prayagraj	Salori - 3	2007	FAB	29	UPJN (Rural)	Achieving
103	Raebareilly	Raebareilly	2022	SBR	18	UPJN (Urban)	Achieving
104	Saharanpur	Mlahipur	1998	UASB	38	UPJN (Urban)	Achieving
105	Saifai	Saifai	2006	Oxidation Pond	1.6	UPJN (Urban)	Not Achieving
106	Varanasi	Bhagwanpur	1994	ASP	8	UPJN (Rural)	Achieving
107	Varanasi	Dinapur	1994	ASP	80	UPJN (Urban)	Achieving
108	Varanasi	DLW	1989	ASP	12	BLW	Achieving
109	Varanasi	Goitha	2018	UASB	120	UPJN (Urban)	Achieving
110	Varanasi	Varanasi GAP-II (JICA)	2018	ASP	140	UPJN (Urban)	Achieving
111	Varanasi	Ramna	2021	SBR	50	UPJN (Rural)	Achieving
112	Varanasi	Ramnagar	2021	A2O	10	UPJN (Rural)	Achieving
113	Vrindavan	Manth Road	2015	UASB	8	UPJN (Urban)	Achieving
114	Vrindavan	Near Pagal Baba Mandir	1998	WSP	4	UPJN (Rural)	Achieving
115	Banda	Kanwara Road	1979	Oxidation Pond	4	UPJN (Urban)	Not operational

116	Bithoor	Bithoor	2020	Wetland	1.3	UPJN (Rural)	Not operational
117	Moradabad	MDA, New Moradabad	2017	SBR	20	Moradabad Development Authority	Not operational
118	Noida	STP 123	2022	SBR	80	Noida	Not operational
119	Rampur	Benajeerpur	2015	UASB	14	UPJN (Urban)	Not operational
120	Rampur	Paharigaon	2015	UASB	15	UPJN (Urban)	Not operational
121	Rampur	Rampur	2017	SBR	5	UPJN (Urban)	Not operational
122	Sultanpur	Lolepur	2002	Oxidation Pond	5	UPJN (Rural)	Not operational
Total Capacity					3860		

Annexure-2

Details of under construction STPs in the State

S. No.	Location	No. of STPs	Capacity MLD	Current Status Physical Progress in %	Implementing Agency	Completion Timeline
1	Ayodhya	1	6	100%	UPJN (Urban)	STP is under trial-run
2	Bareilly	1	35	100%	UPJN (Urban)	STP is under trial-run
3	Pratapgarh	1	8.95	100%	UPJN (Urban)	STP is under trial-run
4	Jaunpur	1	30	98.50%	UPJN (Rural)	STP has been Commissioned.
5	Sultanpur	3	17	96.50%	UPJN (Rural)	Mar-23
6	Naini, Jhansi, Phaphamau	3	72	98.00%	UPJN (Rural)	Naini and Phaphamau STP have been commissioned. Jhansi STP will be commissioned by Mar-23
7	Panka, Kanpur	1	30	96.00%	UPJN (Rural)	STP has been commissioned
8	Aligarh	1	45	95%	UPJN (Urban)	Mar-23
9	Unnao	1	15	94.50%	UPJN (Rural)	Mar-23
10	Gorakhpur	1	5	96%	UPJN (Urban)	Mar-23
11	Shahjahanpur	1	40	90%	UPJN (Urban)	Mar-23
12	Budhana	1	10	87%	UPJN (Rural)	Jun-23
13	Lucknow	1	120	82%	UPJN (Urban)	Mar-23
14	Muzaffarnagar	2	54.5	78.35%	UPJN (Rural)	Jun-23
15	Ghaziabad	1	21.5		Awas Vikas Parishad	Jul-23
16	Shuklaganj	1	5	65%	UPJN (Rural)	Jun-23
17	Jhansi	1	26		Nagar Nigam Jhansi	Aug-23
18	Gorakhpur	1	10	65%	UPJN (Urban)	Apr-23
19	Kairana	1	15	61%	UPJN (Rural)	May-23
20	Balrampur	1	8.5	53%	UPJN (Urban)	Nov-23
21	Mirzapur	2	17	52%	UPJN (Rural)	Jan-24
22	Azamgarh	1	8	42%	UPJN (Urban)	Jan-24
23	Ghazipur	1	21	45%	UPJN (Rural)	Jan-24
24	Bareilly	3	63	54%	UPJN (Rural)	Aug-24
25	Fatehgarh – Farrukhabad	3	45	34%	UPJN (Rural)	Jun-24
26	Lucknow	2	40	29%	UPJN (Rural)	Dec-23
27	Moradabad	1	25	4%	UPJN (Rural)	Dec-24
28	Ayodhya	1	33	8.50%	UPJN (Rural)	Dec-24
29	Agra	13	177.6	3%	UPJN (Rural)	Dec-24
30	Gorakhpur	1	10	2%	UPJN (Urban)	Sep-24
31	Gorakhpur	1	30	2%	UPJN (Urban)	Mar-25
32	Gorakhpur	1	38	2%	UPJN (Urban)	Mar-25
		55	1082			

Details of STPs under tendering Stage in the State

S. No.	Location	No. of STPs	Capacity of STP proposed (MLD)	Status of Tender(Complete or Under Process)	Status of Project	Executing Agency	Timeline
1	Meerut	1	220	Under Process	Clarifications sought by World bank were submitted to NMCG on 22.02.2023. Recommendation to issue LOA to L-1 bidder was intimated vide NMCG letter dated 05.04.2023. UPJN (Rural) response was submitted to NMCG vide letter dated 10.04.2023. NMCG, vide letter dated 14.04.2023 has again requested UPJN (R) for necessary action in this regard. Clarification has been sought from NMCG regarding safeguard measures for Solar Power Plant and open acces policy vide letter dated 18.04.2023.	UPJN (Rural)	Jun-25
2	Saharanpur	1	135	Under Process	Bids have been opened on 23.03.2023. 6 bids have been received which are under evaluation.	UPJN (Rural)	
3	Varanasi	1	55	Under Process	Bids have been opened on 06.03.2023. 9 bids have been received which have been evaluated.	UPJN (Rural)	
4	Mathura	1	60	Under Process	Bids have been opened on 03.04.2023. 4 bids have been received which are under evaluation.	UPJN (Rural)	
5	Kosi	1	12	Under Process	NIT has been issued on 06.04.2023. Last date for submission of bids is 06.05.2023.	UPJN (Rural)	
6	Chhata	1	6	Under Process		UPJN (Rural)	
7	Vrindavan	1	13	Under Process		UPJN (Rural)	
8	Prayagraj (Distt. D)	1	90	Under Process	Last date for submission of bids is 01.05.2023 and it will be opened on 01.05.2023.	UPJN (Rural)	
9	Lucknow	1	50	Under Process	Last date for submission of bids is 24.04.2023 and it will be opened on 25.04.2023.	UPJN (Rural)	
10	Hathras	1	24	Under Process	NIT has been issued on 06.04.2023. Last date for submission of bids is 06.05.2023.	UPJN (Rural)	
11	Prayagraj (Distt. C)	1	43	Under Process	Project has been sanctioned vide NMCG letter dated 14.03.2023. Bid documents have been submitted to NMCG on 01.04.2023.	UPJN (Rural)	
12	Ghaziabad	1	68	Under Process	Technical bid opened on Dt 26.12.2022. Financial bid opened on Dt 23.02.2023. SLTC Meeting held on Dt 02.03.2023. However, Tender have been cancelled and under re-tendering, Technical bid will be opened on 28.04.2023	UPJN (Urban)	
Total		12	776				

Note: 3 projects of Gorakhpur which were earlier in tendering stage are in under construction category (below 50%).

Detail of 317 proposed STPs**A. Details of proposed STPs for which DPR has been submitted by UPJN (Rural) to NMCG**

Sl.	Location	No. of STPs	Capacity of STP proposed (MLD)	Status of DPR	Current Status of DPR	Timeline
1	Lucknow	2	175	DPR is under review in NMCG	DPR is under review in NMCG	Dec-25
2	Varanasi	1	55	DPR is under review in NMCG	DPR is under review in NMCG	
3	Prayagraj	3	55.4	1 DPR is under review in NMCG and 1 DPR is under review in UPJN (R)	1 DPR is under review in NMCG and 1 DPR is to be included as variation in ongoing Namami Gange project at Prayagraj.	
4	Chandauli	1	37	DPR is under review in NMCG	DPR is under review in NMCG	
5	Gorakhpur	1	44	DPR is under review in NMCG	DPR is under review in NMCG	
6	Barhalganj	1	6	DPR is under review in NMCG	DPR is under review in NMCG	
7	Aligarh	2	113	DPR is under review in NMCG	DPR is under review in NMCG	
8	Moradabad	1	43	DPR is under review in NMCG	DPR is under review in NMCG	
9	Deoband	1	17	Land issue resolved. DPR is under preparation by UPJN (R)	Land issue resolved. DPR is under preparation by UPJN ®	
10	Gulaothi	1	10	DPR is under review in NMCG	DPR is under review in NMCG	
11	Hapur	1	6	DPR is under review in NMCG	DPR is under review in NMCG	
12	Shamli	4	60	DPR is under review in NMCG	DPR has been approved during the meeting of 48th Executive committee of NMCG on 18.04.2023	
13	Tanda, Ambedkar nagar	1	15	DPR is under review in UPJN (R)	DPR has been submitted to NMCG after compliance of	

					observations.	
14	Raebareilly	1	0.006	DPR is under review in NMCG	DPR is under review in NMCG	
15	Mau	1	3.5	DPR is under review in NMCG	DPR is under review in NMCG	
16	Manikpur	1	2.4	DPR is under review in NMCG	DPR is under review in NMCG	
	Total	23	642.31			

B. List of approved CSAP prepared by UPJN (Urban) under SBM 2.0

Sl.	District	Name of ULB	Date of Approval SLTC/SHPC	No. of drains (Nala)	Current Status	STP Capacity (MLD)
1	Aligarh	Atruli	05.09.22 / 20.09.22	20	DPR under preparation	5
2	Ambedkarnagar	Iltifatganj Bazar	05.09.22 / 20.09.22	3	DPR prepared and approval awaited	1.5
3	Amethi	Gauriganj (NPP)	01.11.22 / 02.11.22	1	DPR under preparation	2.75
4	Auraiya	Acchalda (NP)	01.11.22 / 02.11.22	2	DPR under preparation	1
5	Auraiya	Auraiya	05.09.22 / 20.09.22	2	DPR under preparation	9
6	Auraiya	Bidhuna (NP)	01.11.22 / 02.11.22	2	DPR under preparation	3.3
7	Ayodhya	Gosaiganj (NP)	01.11.22 / 02.11.22	4	DPR under preparation	1.5
8	Ayodhya	Rudauli (NPP)	01.11.22 / 02.11.22	5	DPR under preparation	4.5
9	Azamgarh	Mubarakpur(NPP)	01.11.22 / 02.11.22	11	DPR under preparation	12
10	Baghpat	Baghpat (NPP)	01.11.22 / 02.11.22	4	DPR prepared and under observation	0
11	Balrampur	Tulsipur (NP)	01.11.22 / 02.11.22	5	DPR under preparation	3.25
12	Balrampur	Utraula (NPP)	01.11.22 / 02.11.22	2	DPR under preparation	3.25
13	Bareilly	Aonla	01.11.22 / 02.11.22	36	DPR prepared and approval awaited	6
14	Bareilly	Faridpur	05.09.22 / 20.09.22	15	DPR prepared and approval awaited	10
15	Bijnor	Kiratpur	05.09.22 / 20.09.22	7	DPR prepared and approval awaited	6.5
16	Bijnor	Najibaabad	05.09.22 / 20.09.22	8	DPR under preparation	9
17	Bijnor	Nagina	05.09.22 / 20.09.22	8	DPR under preparation	10
18	Bijnor	Chandpur	05.09.22 / 20.09.22	28	DPR prepared and approval awaited	8.5
19	Bijnor	Sherkot	05.09.22 / 20.09.22	6	DPR under preparation	6.5
20	Bijnor	Dhampur	05.09.22 / 20.09.22	16	DPR prepared and approval awaited	5
21	Bulandshahr	Aurangabad(NP)	01.11.22 / 02.11.22	17	DPR prepared and approval awaited	2.82
22	Bulandshahr	Sikandrabad(NPP)	01.11.22 / 02.11.22	14	DPR under preparation	8.4

23	Bulandshahr	B.B. Nagar (NP)	01.11.22 / 02.11.22	7	DPR prepared and approval awaited	0.97
24	Bulandshahr	Narora (NP)	01.11.22 / 02.11.22	8	DPR prepared and approval awaited	0
25	Bulandshahr	Gulaothi (NPP)	01.11.22 / 02.11.22	2	DPR under preparation	5
26	Bulandshahr	Debai (NPP)	01.11.22 / 02.11.22	8	DPR under preparation	3.8
27	Bulandshahr	Siana (NPP)	01.11.22 / 02.11.22	5	DPR under preparation	4.5
28	Bulandshahr	Chhatari (NP)	01.11.22 / 02.11.22	3	DPR prepared and approval awaited	1.2
29	Bulandshahr	Anupshahar(NPP)	01.11.22 / 02.11.22	13	DPR prepared and approval awaited	0
30	Bulandshahr	Bugrasi (NP)	01.11.22 / 02.11.22	5	DPR under preparation	1.5
31	Bulandshahr	Jahangirabad(NPP)	01.11.22 / 02.11.22	1	DPR under preparation	6
32	Chitrakoot	Chitrakoot Dham Karwi (NPP)	01.11.22 / 02.11.22	10	DPR under preparation	9.5
33	Chitrakoot	Rajapur (NP)	01.11.22 / 02.11.22	5	DPR prepared and under observation	2.5
34	Deoria	Bariyarpur(NP)	01.11.22 / 02.11.22	1	DPR under preparation	2.84
35	Deoria	Lar	05.09.22 / 20.09.22	3	DPR prepared and approval awaited	3
36	Deoria	Gaura Barhaj	05.09.22 / 20.09.22	11	DPR prepared and approval awaited	5
37	Etawah	Bakewar (NP)	01.11.22 / 02.11.22	2	DPR under preparation	1.6
38	Etawah	Jasawantnagar(NPP)	01.11.22 / 02.11.22	2	DPR under preparation	3.3
39	Farrukhabad	Shamshabad	05.09.22 / 20.09.22	3	DPR prepared and approval awaited	8
40	Farrukhabad	Kampil	05.09.22 / 20.09.22	4	DPR prepared and approval awaited	2
41	G B Nagar	Dadri (NPP)	01.11.22 / 02.11.22	27	DPR under preparation	10.56
42	Ghaziabad	Muradnagar (NPP)	01.11.22 / 02.11.22	17	DPR under preparation	10.19
43	Ghaziabad	Niwari (NP)	01.11.22 / 02.11.22	3	DPR under preparation	1
44	Ghaziabad	Faridnagar (NP)	01.11.22 / 02.11.22	3	DPR prepared and approval awaited	1.25
45	Ghaziabad	Patala (NP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	1
46	Ghaziabad	Dasna (NP)	01.11.22 / 02.11.22	2	DPR under preparation	3.5
47	Hapur	Pilkhuwa(NPP)	01.11.22 / 02.11.22	8	DPR prepared and approval awaited	6
48	Hardoi	Shahabad	01.11.22 / 02.11.22	15	DPR under preparation	10.25
49	Jalaun	Jalaun	05.09.22 / 20.09.22	3	DPR under preparation	6
50	Jalaun	Kalpi	05.09.22 / 20.09.22	2	DPR under preparation	6
51	Jalaun	Konch	05.09.22 / 20.09.22	2	DPR under preparation	6
52	Jaunpur	kerakat(NP)	01.11.22 / 02.11.22	3	DPR under preparation	1.34
53	Jaunpur	Shahganj(NPP)	01.11.22 /	4	DPR under	2.71

			02.11.22		preparation	
54	Jaunpur	Badlapur(NP)	01.11.22 / 02.11.22	4	DPR under preparation	2.08
55	Jaunpur	Zafrabad(NP)	01.11.22 / 02.11.22	6	DPR under preparation	1.13
56	Jaunpur	Gaurabadshahpur (NP)	01.11.22 / 02.11.22	3	DPR under preparation	2.32
57	Jaunpur	Kajgaon(NP)	01.11.22 / 02.11.22	4	DPR under preparation	1.35
58	Jaunpur	Kheta sarai (NP)	01.11.22 / 02.11.22	4	DPR under preparation	1.9
59	Jaunpur	Mugrabadshahpur(NPP)	01.11.22 / 02.11.22	2	DPR preared and under observation	3.09
60	Jaunpur	Machhlishahr(NP)	01.11.22 / 02.11.22	5	DPR under preparation	2.51
61	Jaunpur	Mariahu(NP)	01.11.22 / 02.11.22	4	DPR under preparation	2.2
62	Jaunpur	Rampur (NP)	01.11.22 / 02.11.22	1	DPR under preparation	1.58
63	Kannauj	Chhibramau	05.09.22 / 20.09.22	2	DPR prepared and approval awaited	12
64	Kanpur Dehat	Akbarpur	05.09.22 / 20.09.22	13	DPR under preparation	4.5
65	Kaushambi	Manjhanpur	05.09.22 / 20.09.22	2	DPR under preparation	10.5
66	Kushinagar	Chhitauni(NP)	01.11.22 / 02.11.22	1	DPR under preparation	2.5
67	Kushinagar	Dudahi(NP)	01.11.22 / 02.11.22	2	DPR under preparation	2.5
68	Kushinagar	Khadda(NP)	01.11.22 / 02.11.22	1	DPR under preparation	1.6
69	Kushinagar	Ramkola(NP)	01.11.22 / 02.11.22	4	DPR under preparation	8
70	Lakhimpur	GolaGokarnnath	05.09.22 / 20.09.22	6	DPR prepared and approval awaited	6.15
71	Lucknow	Kakori (NP)	01.11.22 / 02.11.22	9	DPR under preparation	2
72	Lucknow	Malihabad (NP)	01.11.22 / 02.11.22	8	DPR under preparation	2.5
73	Maharajganj	Maharajganj(NPP)	01.11.22 / 02.11.22	8	DPR under preparation	6.5
74	Maharajganj	Nichlaul(NP)	01.11.22 / 02.11.22	3	DPR under preparation	2
75	Maharajganj	Nautanwa (NPP)	01.11.22 / 02.11.22	5	DPR under preparation	3.64
76	Maharajganj	Sonauli (NP)	01.11.22 / 02.11.22	2	DPR under preparation	2.21
77	Mathura	Gokul (NP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	0.6
78	Mathura	Goverdhan (NP)	01.11.22 / 02.11.22	3	DPR under preparation	4.5
79	Mathura	Mahavan (NP)	01.11.22 / 02.11.22	2	DPR prepared and approval awaited	1.2
80	Meerut	Sardhana (NPP)	01.11.22 / 02.11.22	3	DPR under preparation	6
81	Moradabad	Bilari (NPP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	3.8
82	Moradabad	Kanth (NP)	01.11.22 / 02.11.22	1	DPR under preparation	2.6
83	Moradabad	Umrikalan (NP)	01.11.22 / 02.11.22	2	DPR under preparation	1.8
84	Moradabad	Kundarki (NP)	01.11.22 / 02.11.22	4	DPR under preparation	3
85	Muzaffarnagar	Purkazi (NP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	2.77
86	Muzaffarnagar	Miranpur (NP)	01.11.22 /	4	DPR under	2.8

			02.11.22		preparation	
87	Muzaffarnagar	Jansath (NP)	01.11.22 / 02.11.22	7	DPR prepared and approval awaited	2
88	Muzaffarnagar	Shahpur (NP)	01.11.22 / 02.11.22	3	DPR prepared and approval awaited	2.1
89	Muzaffarnagar	Khatauli	05.09.22 / 20.09.22	3	DPR prepared and approval awaited	7.5
90	Pratapgarh	Bela Pratapgarh (NPP)	01.11.22 / 02.11.22	26	DPR under preparation	3
91	Pratapgarh	Lalganj	05.09.22 / 20.09.22	2	DPR under preparation	2.75
92	Prayagraj	Bharatganj (NP)	01.11.22 / 02.11.22	3	DPR under preparation	1.7
93	Prayagraj	Phulpur (NP)	01.11.22 / 02.11.22	5	DPR under preparation	2.3
94	Prayagraj	Mau Aima (NP)	01.11.22 / 02.11.22	7	DPR under preparation	2.06
95	Prayagraj	Sirsa (NP)	01.11.22 / 02.11.22	3	DPR under preparation	1.27
96	Raebareilly	Salon	05.09.22 / 20.09.22	3	DPR under preparation	1.5
97	Rampur	Kemri(NP)	01.11.22 / 02.11.22	3	DPR prepared and approval awaited	2.9
98	Rampur	Tanda(NPP)	01.11.22 / 02.11.22	8	DPR prepared and approval awaited	4.8
99	Rampur	Dariyal(NP)	01.11.22 / 02.11.22	5	DPR under preparation	2.1
100	Rampur	Suar(NPP)	01.11.22 / 02.11.22	6	DPR under preparation	3.2
101	Rampur	Bilaspur(NPP)	01.11.22 / 02.11.22	6	DPR prepared and approval awaited	4.5
102	Rampur	Maswasi(NP)	01.11.22 / 02.11.22	5	DPR under preparation	1.8
103	Rampur	Milak(NPP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	3.1
104	Rampur	NarpatNagar(NP)	01.11.22 / 02.11.22	12	DPR under preparation	2.1
105	Rampur	Shahabad(NP)	01.11.22 / 02.11.22	4	DPR prepared and approval awaited	3.8
106	Rampur	Saifni(NP)	01.11.22 / 02.11.22	2	DPR prepared and approval awaited	2.2
107	Saharanpur	Ambetha (NP)	01.11.22 / 02.11.22	6	DPR prepared and under observation	1.5
108	Saharanpur	Chhutmalpur(NP)	01.11.22 / 02.11.22	8	DPR prepared and approval awaited	2.5
109	Saharanpur	Chilkana Sultanpur(NP)	01.11.22 / 02.11.22	10	DPR under preparation	2
110	Saharanpur	Gangho (NP)	01.11.22 / 02.11.22	5	DPR under preparation	5.5
111	Saharanpur	Nakur (NPP)	01.11.22 / 02.11.22	10	DPR under preparation	2
112	Saharanpur	Nanauta (NP)	01.11.22 / 02.11.22	6	DPR under preparation	2.4
113	Saharanpur	Rampur Maniharan (NP)	01.11.22 / 02.11.22	10	DPR under preparation	3.28
114	Saharanpur	Sarsawa (NPP)	01.11.22 / 02.11.22	3	DPR under preparation	2
115	Saharanpur	Titron (NP)	01.11.22 / 02.11.22	5	DPR under preparation	1
116	Saharanpur	Behat (NP)	01.11.22 / 02.11.22	4	DPR under preparation	2
117	Sant Kabir Nagar	Maghar	05.09.22 /	2	DPR under	2

			20.09.22		preparation	
118	Sant KabirNagar	Bakhira (NP)	01.11.22 / 02.11.22	3	DPR under preparation	4.13
119	Sant KabirNagar	Belharkala (NP)	01.11.22 / 02.11.22	1	DPR under preparation	1.53
120	Sant Kabir Nagar	Mehandawal(NP)	01.11.22 / 02.11.22	1	DPR under preparation	5.5
121	Sant KabirNagar	Hariharpur (NP)	01.11.22 / 02.11.22	1	DPR under preparation	1.18
122	Sant Kabir Nagar	Khalilabad	05.09.22 / 20.09.22	1	DPR under preparation	7.4
123	Sitapur	Biswan (NPP)	01.11.22 / 02.11.22	7	DPR under preparation	5.77
124	Sitapur	Mahmudabad(NPP)	01.11.22 / 02.11.22	5	DPR under preparation	5.25
125	Sitapur	Maholi (NP)	01.11.22 / 02.11.22	2	DPR prepared and approval awaited	3.13
126	Sitapur	Hargaon (NP)	01.11.22 / 02.11.22	2	DPR prepared and approval awaited	2.23
127	Sitapur	Khairabad(NPP)	01.11.22 / 02.11.22	2	DPR under preparation	5.01
128	Sitapur	Sidhauli (NP)	01.11.22 / 02.11.22	3	DPR under preparation	2.58
129	Sonbhadra	Obra (NP)	01.11.22 / 02.11.22	8	DPR under preparation	6
130	Sonebhadra	Anpara (NP)	01.11.22 / 02.11.22	12	DPR under preparation	7.5
131	Sonebhadra	Robertsganj (NPP)	01.11.22 / 02.11.22	2	DPR under preparation	6.1
132	Srawasti	Bhingra (NPP)	01.11.22 / 02.11.22	5	DPR under preparation	5
133	Srawasti	Ikauna (NP)	01.11.22 / 02.11.22	11	DPR under preparation	1.5
134	Unnao	Bangermau(NPP)	01.11.22 / 02.11.22	12	DPR under preparation	5
135	Unnao	Gangaghat(NPP)	01.11.22 / 02.11.22	13	DPR preared and under observation	8
136	Unnao	Nawabganj (NP)	01.11.22 / 02.11.22	2	DPR preared and under observation	1.2
137	Unnao	Safipur (NP)	01.11.22 / 02.11.22	3	DPR prepared and approval awaited	2.4
138	Unnao	Ganj muradabad (NP)	01.11.22 / 02.11.22	7	DPR under preparation	1
139	Unnao	Auras (NP)	01.11.22 / 02.11.22	1	DPR under preparation	1
140	Ambedkarnagar	Jalalpur (NPP)	06.03.23	9	DPR under preparation	5.5
141	Ambedkar nagar	Ashrafpur Kicchoucha (NP)	06.03.23	6	DPR under preparation	3.8
142	Amethi	Jais (NP)	06.03.23	4	DPR under preparation	4
143	Amroha	Bachhraun (NPP)	06.03.23	24	DPR under preparation	3.1
144	Amroha	Hasanpur (NPP)	06.03.23	4	DPR under preparation	6.1
145	Amroha	Joya (NP)	06.03.23	2	DPR under preparation	2.2
146	Amroha	Naugawan Sadat (NP)	06.03.23	5	DPR under preparation	3.4
147	Amroha	Said Nagli (NP)	06.03.23	5	DPR under preparation	1.9
148	Amroha	Ujhari (NP)	06.03.23	4	DPR under preparation	2.6
149	Amroha	Dhanaura (NPP)	06.03.23	1	DPR under preparation	3.1
150	Amroha	Gajraula (NPP)	06.03.23	6	DPR under preparation	6.5
151	Azamgarh	Atrauliya (NP)	06.03.23	4	DPR under	1.2

					preparation	
152	Azamgarh	Jiyanpur (NP)	06.03.23	5	DPR under preparation	1.25
153	Ballia	Chitbaragoan (NP)	06.03.23	3	DPR under preparation	2.1
154	Balrampur	Balrampur (NP)	06.03.23	5	DPR under preparation	8.33
155	Bareilly	Baheri (NPP)	06.03.23	3	DPR under preparation	7
156	Basti	Rudhauri Bazar (NP)	06.03.23	2	DPR under preparation	-
157	Bhadohi	Gyanpur (NP)	06.03.23	2	DPR under preparation	1.32
158	Budaun	Faizganj (NP)	06.03.23	2	DPR under preparation	1.25
159	Budaun	Bisauli (NPP)	06.03.23	10	DPR under preparation	3.5
160	Budaun	Kuwargaon (NP)	06.03.23	3	DPR under preparation	0.8
161	Budaun	Ujhani (NPP)	06.03.23	10	DPR under preparation	6
162	Budaun	Saidpur (NP)	06.03.23	3	DPR under preparation	1.4
163	Budaun	Wazirganj (NP)	06.03.23	3	DPR under preparation	2.1
164	Budaun	Dataganj (NPP)	06.03.23	3	DPR under preparation	2.7
165	Budaun	Gulariya (NP)	06.03.23	4	DPR under preparation	0.4
166	Budaun	Alapur (NP)	06.03.23	5	DPR under preparation	2.3
167	Budaun	Sakhanu (NP)	06.03.23	6	DPR under preparation	1
168	Budaun	Usawan (NP)	06.03.23	5	DPR under preparation	1.2
169	Chandauli	Chakia (NP)	06.03.23	1	DPR under preparation	1.73
170	Chandauli	Chandauli (NP)	06.03.23	1	DPR under preparation	2.62
171	Chandauli	Saiyad raja (NP)	06.03.23	2	DPR under preparation	1.86
172	Farrukhabad	Kaimganj (NPP)	06.03.23	4	DPR under preparation	3.4
173	Farrukhabad	Mahommadabad (NP)	06.03.23	3	DPR under preparation	2.5
174	Fatehpur	Bindki (NPP)	06.03.23	3	DPR under preparation	3.64
175	Fatehpur	Khaga (NP)	06.03.23	2	DPR under preparation	6.1
176	Fatehpur	Kora Jahanabad (NP)	06.03.23	2	DPR under preparation	2.71
177	FIROZABAD	Sirsaganj (NPP)	06.03.23	4	DPR under preparation	3.52
178	FIROZABAD	Jasrana (NP)	06.03.23	5	DPR under preparation	1.05
179	FIROZABAD	Fariha (NP)	06.03.23	3	DPR under preparation	0.68
180	FIROZABAD	Eka (NP)	06.03.23	2	DPR under preparation	2.69
181	Ghazipur	Saidpur (NP)	06.03.23	8	DPR under preparation	2.5
182	GORAKHPUR	Barharganj (NP)	06.03.23	7	DPR under preparation	-
183	GORAKHPUR	Gola (NP)	06.03.23	7	DPR under preparation	4.45
184	GORAKHPUR	Mundera Bazar (NP)	06.03.23	9	DPR under preparation	2.92
185	GORAKHPUR	Unwal (NP)	06.03.23	3	DPR under preparation	2.06
186	GORAKHPUR	Bansgaon (NP)	06.03.23	5	DPR under preparation	1.6
187	GORAKHPUR	Sahjanwa (NP)	06.03.23	3	DPR under preparation	3.45

188	GORAKHPUR	Campierganj (NP)	06.03.23	2	DPR under preparation	2.28
189	GORAKHPUR	Pipiganj (NP)	06.03.23	3	DPR under preparation	5.01
190	GORAKHPUR	Pipraich (NP)	06.03.23	2	DPR under preparation	3.54
191	Hamirpur	Hamirpur (NPP)	06.03.23	11	DPR under preparation	5.75
192	Hamirpur	Rath (NP)	06.03.23	11	DPR under preparation	6.78
193	Jalaun	Madhogarh (NP)	06.03.23	3	DPR under preparation	1.3
194	Jalaun	Nadigaon (NP)	06.03.23	2	DPR under preparation	0.8
195	Jalaun	Umri (NP)	06.03.23	1	DPR under preparation	1
196	Jalaun	Kotra (NP)	06.03.23	4	DPR under preparation	0.8
197	Jalaun	Rampura (NP)	06.03.23	3	DPR under preparation	1.3
198	Jalaun	Kadaura (NP)	06.03.23	3	DPR under preparation	1.6
199	Jalaun	Ait (NP)	06.03.23	2	DPR under preparation	1.33
200	Jhansi	Baragaon (NP)	06.03.23	6	DPR under preparation	1
201	Jhansi	Barua Sagar (NP)	06.03.23	6	DPR under preparation	2.5
202	Jhansi	Ranipur (NP)	06.03.23	6	DPR under preparation	2
203	Jhansi	Mauranipur(NPP)	06.03.23	15	DPR under preparation	6
204	Jhansi	Chirgaon(NPP)	06.03.23	5	DPR under preparation	2
205	Kannauj	Gursahayganj (NPP)	06.03.23	1	DPR under preparation	5.7
206	Kannauj	Tirwaganj (NP)	06.03.23	4	DPR under preparation	3
207	Kannauj	Kannauj (NPP)	06.03.23	3	DPR under preparation	3.5
208	Kannauj	Talgram (NP)	06.03.23	2	DPR under preparation	1.1
209	Kannauj	Samdhan (NP)	06.03.23	3	DPR under preparation	3.5
210	Kannauj	Sikandarpur(NP)	06.03.23	4	DPR under preparation	1
211	Kanpur Dehat	Pukhrayan (NPP)	06.03.23	8	DPR under preparation	5
212	Kanpur Dehat	Sikandra (NP)	06.03.23	6	DPR under preparation	1.4
213	Kanpur Dehat	Rajpur (NP)	06.03.23	14	DPR under preparation	1.78
214	Kanpur Dehat	Raniya (NP)	06.03.23	14	DPR under preparation	2.82
215	Kanpur Dehat	Shivli (NP)	06.03.23	8	DPR under preparation	1.6
216	Kanpur Dehat	Derapur (NP)	06.03.23	5	DPR under preparation	0.8
217	Kanpur Dehat	Amraudha (NP)	06.03.23	7	DPR under preparation	1
218	Kanpur Dehat	Rasulabad (NP)	06.03.23	6	DPR under preparation	2.21
219	Kanpur Dehat	Jhinhak (NP)	06.03.23	21	DPR under preparation	2.41
220	Kanpur Dehat	Kanchausi (NP)	06.03.23	6	DPR under preparation	1.74
221	Kanpur Dehat	Musanagar (NP)	06.03.23	11	DPR under preparation	2.1
222	Kanpur Dehat	Rura (NP)	06.03.23	14	DPR under preparation	1.85
223	Kanpur Nagar	Ghatampur (NP)	06.03.23	5	DPR under preparation	5.86
224	Kaushambi	Purab pashchim sharira	06.03.23	3	DPR under	2.21

		(NP)			preparation	
225	Kaushambi	Charwa (NP)	06.03.23	1	DPR under preparation	1.98
226	Kaushambi	Daranagar Kadadham (NP)	06.03.23	4	DPR under preparation	2.2
227	Lakhimpur	Mailani (NP)	06.03.23	2	DPR under preparation	1.39
228	Lakhimpur	Barwar (NP)	06.03.23	3	DPR under preparation	1.46
229	Lakhimpur	Nighasan (NP)	06.03.23	2	DPR under preparation	2.53
230	Lakhimpur	Oel Dakhwa(NP)	06.03.23	3	DPR under preparation	1.34
231	Lakhimpur	Sighahi Bhiraure (NP)	06.03.23	3	DPR under preparation	1.99
232	Lakhimpur	Kheri (NP)	06.03.23	2	DPR under preparation	3.47
233	Lakhimpur	Mohamdi (NPP)	06.03.23	3	DPR under preparation	4.89
234	Lakhimpur	Dhaurahra (NP)	06.03.23	2	DPR under preparation	3.14
235	Lakhimpur	Paliya Kalan(NPP)	06.03.23	1	DPR under preparation	4.26
236	Lalitpur	Talbehat (NP)	06.03.23	10	DPR under preparation	1.5
237	Mahoba	Mahoba (NPP)	06.03.23	5	DPR under preparation	10.01
238	Mau	Adari (NP)	06.03.23	5	DPR under preparation	1.5
239	MAU	Ghosi (NP)	06.03.23	7	DPR under preparation	4.5
240	MAU	Kopaganj (NP)	06.03.23	5	DPR under preparation	5.5
241	MAU	Mohammadabad Gohna(NP)	06.03.23	3	DPR under preparation	4.25
242	Meerut	Daurala (NP)	06.03.23	4	DPR under preparation	2
243	Meerut	Harra (NP)	06.03.23	1	DPR under preparation	2
244	Meerut	Hastinapur (NP)	06.03.23	4	DPR under preparation	2.75
245	Meerut	Karnawal (NP)	06.03.23	2	DPR under preparation	1.3
246	Meerut	Khiwai (NP)	06.03.23	7	DPR under preparation	2.2
247	Meerut	Lawad (NP)	06.03.23	8	DPR under preparation	2.1
248	Meerut	Mawana (NP)	06.03.23	2	DPR under preparation	7.79
249	Mirzapur	Chunar (NPP)	06.03.23	5	DPR under preparation	3.79
250	Mirzapur	Ahaura (NPP)	06.03.23	1	DPR under preparation	2.41
251	Mirzapur	Kachhawa (NP)	06.03.23	2	DPR under preparation	1.25
252	Pilibhit	Bisalpur (NPP)	06.03.23	6	DPR under preparation	8
253	Pilibhit	Bilsabda (NP)	06.03.23	8	DPR under preparation	2
254	Pilibhit	Jahanabad (NP)	06.03.23	8	DPR under preparation	2
255	Pratapgarh	Antu (NP)	06.03.23	2	DPR under preparation	1.15
256	Pratapgarh	Dhakawaa (NP)	06.03.23	2	DPR under preparation	2
257	Pratapgarh	Katra Medniganj	06.03.23	1	DPR under preparation	1.05
258	Pratapgarh	Kohdaur (NP)	06.03.23	2	DPR under preparation	1.6
259	Pratapgarh	Kunda (NP)	06.03.23	7	DPR under preparation	2.75
260	Pratapgarh	Manikpur (NP)	06.03.23	5	DPR under preparation	1.6

261	Pratapgarh	Patti (NP)	06.03.23	4	DPR under preparation	1.1
262	Pratapgarh	Prithviganj (NP)	06.03.23	4	DPR under preparation	2.4
263	Pratapgarh	Pratapgarh city(NP)	06.03.23	3	DPR under preparation	1.6
264	Pratapgarh	Ramganj (NP)	06.03.23	4	DPR under preparation	2
265	Pratapgarh	Raniganj (NP)	06.03.23	3	DPR under preparation	3
266	Pratapgarh	Suvansha bazar(NP)	06.03.23	1	DPR under preparation	2.3
267	Prayagraj	Lalgopal ganj(NP)	06.03.23	2	DPR under preparation	2.9
268	Prayagraj	Handia(NP)	06.03.23	4	DPR under preparation	2.3
269	Raebareli	Unchahar (NP)	06.03.23	12	DPR under preparation	1
270	Raebareli	Maharajganj(NP)	06.03.23	4	DPR under preparation	1
271	Raebareli	Bachhrawan(NP)	06.03.23	11	DPR under preparation	1
272	Raebareli	Naseerabad (NP)	06.03.23	5	DPR under preparation	2
273	Raebareli	Lalgang (NP)	06.03.23	13	DPR under preparation	2.5
274	Raebareli	Parsadepur (NP)	06.03.23	5	DPR under preparation	2
275	Raebareli	Dalmau (NP)	06.03.23	9	DPR under preparation	1
276	Sambhal	Babrala (NP)	06.03.23	4	DPR under preparation	1.9
277	Sambhal	Bahjoi (NPP)	06.03.23	6	DPR under preparation	3.7
278	Sambhal	Gawan (NP)	06.03.23	6	DPR under preparation	1
279	Sambhal	Gunnaur (NP)	06.03.23	4	DPR under preparation	2.4
280	Sambhal	Narauli (NP)	06.03.23	4	DPR under preparation	1.8
281	Sambhal	Sirsi (NP)	06.03.23	7	DPR under preparation	2.7
282	Shahajahanpur	Tilhar (NPP)	06.03.23	7	DPR under preparation	6
283	Shahajahanpur	Khudaganj (NP)	06.03.23	4	DPR under preparation	1.5
284	Shahajahanpur	Katra (NP)	06.03.23	6	DPR under preparation	3.25
285	Shahajahanpur	Jalalabad (NPP)	06.03.23	8	DPR under preparation	3.8
286	Shahajahanpur	Khutar (NP)	06.03.23	8	DPR under preparation	2
287	Shahajahanpur	Banda (NP)	06.03.23	2	DPR under preparation	2
288	Shahajahanpur	Nigohi (NP)	06.03.23	4	DPR under preparation	2.5
289	Sitapur	Laharpur (NPP)	06.03.23	8	DPR under preparation	6.41
290	Sitapur	Paitepur (NP)	06.03.23	2	DPR under preparation	1.44
291	Sitapur	Tambour- Ahmdabad (NP)	06.03.23	2	DPR under preparation	2.7
292	Sonbhadra	Pipari (NP)	06.03.23	6	DPR under preparation	1.6
293	Sonbhadra	Dala Bazar (NP)	06.03.23	3	DPR under preparation	1.1
294	Sonbhadra	Ghorawal (NP)	06.03.23	1	DPR under preparation	0.8
295	Sonbhadra	Renukot (NP)	06.03.23	2	DPR under preparation	2.1
296	Sonbhadra	Churk-Ghurma(NP)	06.03.23	5	DPR under preparation	0.7

297	Sonbhadra	Chopan (NP)	06.03.23	3	DPR under preparation	1.3
298	Sonbhadra	Duddhi (NP)	06.03.23	2	DPR under preparation	1.1
299	Varanasi	Gangapur (NP)	06.03.23	2	DPR under preparation	0.84
Total (294 STPs)				1602		950.87

Annexure-5

Status of CETP								
S.N	District	Name and Address of the CETPs	Operated by	Capacity (MLD)	Nature of Member Units	Operational Status	Observed final effluent quality	Name of treated Effluent receiving water body Drain/Sub-Tributary/ River
1	Hapur	CETP, HPDA, Pilkhaun, Hapur	HPDA	2.1 MLD	Textile	Operational	Achieving	River Ganga through River Kali East
2	Kanpur	CETP, UPSIDC Textile Complex, Rooma, Kanpur (for textile units)	UPSIDC/ Rooma Pollution Control Association	1.5 MLD	Textile	Operational	Achieving	On Land
3	Ghaziabad	Apparel Park Tronica City CETP, Phase-I (for textile units), Ghaziabad	UPSIDC	6 MLD	Textile	Operational	Achieving	River Yamuna Through Hindon River
4	Mathura	CETP, Industrial Area, Site-A, Mathura	Industrial Association	6.25 MLD,	Textile	Operational	Achieving	River Yamuna
5	Unnao	Banther Industrial Pollution Control Co. CETP, Banther, Unnao	Banther Industrial Pollution Control Co.	4.5 MLD	Tannery	Operational	Achieving	River Ganga
6	Unnao	Unnao Tanneries Pollution Control Company (CETP) Site-II, Unnao	Unnao Tanneries Pollution Control Company	2.15 MLD	Tannery	Operational	Achieving	River Ganga
7	Kanpur	CETP Jajmau, Kanpur	U.P. Jal Nigam	36 MLD	Tannery	Operational	Not Achieving	Irrigation Channel

Annexure-6.1

Solid Waste Prograss Report					
Current Status					
19 Plants					
S.N.	District	ULB	Capacity	Authorization Valid Up to	Current Status (Oprational/Non-Oprational)
1	Hapur	Pilkhuwa	45	17-03-2028	Operational
2	Prayagraj	Prayagraj	400	15-03-2028	Operational
3	Kannauj	Kannauj	25	15-03-2028	Operational
4	Kanpur	Kanpur	1500	02-04-2028	Operational
5	Muzaffarnagar	Muzaffarnagar	120	16-03-2028	Operational
6	Aligarh	Aligarh	220	16-03-2028	Operational
7	Etawah	Etawah	75	14-04-2027	Operational
8	Mathura	Mathura Vrindavan	180	16-03-2028	Operational
9	Agra	Agra	300	01-07-2024	Operational
10	Barabanki	Nawabganj	100	27-03-2028	Operational
11	Lucknow	Lucknow	1300	16-03-2027	Operational
12	Varanasi	Varanasi	600	31-12-2027	Operational
13	Jaunpur	Jaunpur	60	31-12-2027	Operational
14	Ballia	Bailla	50	Not Granted	Operational
15	Azamgarh	Mubarakpur	40	31-12-2027	Operational
16	Moradabad	Moradabad	400	31-12-2027	Operational
17	Noida	Noida	380	—	Operational
18	Ballia	Reoti	10	Applied For Authorization	Operational
19	Shahjahanpur	Shahjahanpur	90	Applied For Authorization	Operational
Total			5895		

Solid Waste Progress Report					
Current Status					
535 MRFs Plants					
S.No.	District	ULBs	Capacity (TPD)	Status(Operational/Non-Operational)	Issues related to progress
1	Agra	Achhnera (NPP)	5	Operational	
2	Agra	Agra (M.Corp)	5	Operational	
3	Agra	Bah (NPP)	5	Operational	
4	Agra	Dayalbagh (NP)	5	Operational	
5	Agra	Etmadpur (NPP)	5	Operational	
6	Agra	Fatehpur Sikri (NPP)	5	Operational	
7	Agra	Jagner (NP)	5	Operational	
8	Agra	Kheragarh (NP)	5	Operational	
9	Agra	Kiraoali (NP)	5	Operational	
10	Agra	Pinahat (NP)	5	Operational	
11	Agra	Shamsabad (NPP)	5	Operational	
12	Agra	Swamibagh (NP)	5	Operational	
13	Firozabad	Eka (NP)	5	Operational	
14	Firozabad	Fariha (NP)	5	Operational	
15	Firozabad	Firozabad (M Corp.)	5	Operational	
16	Firozabad	MAKKHANPUR	5	Operational	
17	Firozabad	Shikohabad (NPP)	5	Operational	
18	Firozabad	Sirsaganj (NPP)	5	Operational	
19	Firozabad	Tundla (NPP)	5	Operational	
20	Mainpuri	BARNAHAL	5	Operational	
21	Mainpuri	Bewar (NP)	5	Operational	
22	Mainpuri	Bhogaon (NP)	5	Operational	
23	Mainpuri	Ghiraun (NP)	5	Operational	
24	Mainpuri	Jyoti Khuriya (NP)	5	Operational	
25	Mainpuri	Karhal (NP)	5	Operational	
26	Mainpuri	Kishni (NP)	5	Operational	
27	Mainpuri	Kuraoali (NP)	5	Operational	
28	Mainpuri	Kushmara (NP)	5	Operational	
29	Mainpuri	Mainpuri (NPP)	5	Operational	
30	Mathura	Bajna (NP)	5	Operational	
31	Mathura	Baldeo (NP)	5	Operational	
32	Mathura	Barsana (NP)	5	Operational	
33	Mathura	Chaumuhan (NP)	5	Operational	
34	Mathura	Chhata (NP)	5	Operational	
35	Mathura	Farah (NP)	5	Operational	
36	Mathura	Gokul (NP)	5	Operational	
37	Mathura	Govardhan (NP)	5	Operational	
38	Mathura	Mahavan (NP)	5	Operational	
39	Mathura	Mathura (M Corp.)	5	Operational	
40	Mathura	Nandgaon (NP)	5	Operational	
41	Mathura	Radhakund (NP)	5	Operational	
42	Mathura	Saunkh (NP)	5	Operational	
43	Aligarh	Aligarh (M Corp.)	5	Operational	
44	Aligarh	Atrauli (NPP)	5	Operational	
45	Aligarh	Beswan (NP)	5	Operational	
46	Aligarh	CHANDAUS	5	Operational	
47	Aligarh	Chharra (NP)	5	Operational	
48	Aligarh	Harduaganj (NP)	5	Operational	
49	Aligarh	Iglas (NP)	5	Operational	
50	Aligarh	Jalali (NP)	5	Operational	
51	Aligarh	Jattari (NP)	5	Operational	
52	Aligarh	JAWAN SIKANDARPUR (NP)	5	Operational	
53	Aligarh	Kauriaganj (NP)	5	Operational	
54	Aligarh	Khair (NPP)	5	Operational	
55	Aligarh	Pilkhana (NP)	5	Operational	
56	Aligarh	Vijaigarh (NP)	5	Operational	
57	Etah	Aliganj (NPP)	5	Operational	
58	Etah	Awagarh (NP)	5	Operational	
59	Etah	Etah (NPP)	5	Operational	
60	Etah	Jaithara (NP)	5	Operational	
61	Etah	Jalesar (NPP)	5	Operational	
62	Etah	Marehra (NPP)	5	Operational	
63	Etah	Nidhauli Kalan (NP)	5	Operational	
64	Etah	Raja Ka Rampur (NP)	5	Operational	
65	Etah	Sakit (NP)	5	Operational	

66	Hathras	Hasayan (NP)	5	Operational	
67	Hathras	Hathras (NPP)	5	Operational	
68	Hathras	Mendu (NP)	5	Operational	
69	Hathras	Purdilnagar (NP)	5	Operational	
70	Hathras	Sadabad (NP)	5	Operational	
71	Hathras	Sahpau (NP)	5	Operational	
72	Hathras	Sasni (NP)	5	Operational	
73	Kasganj	Amapur (NP)	5	Operational	
74	Kasganj	Bhargain (NP)	5	Operational	
75	Kasganj	Kasganj (NPP)	5	Operational	
76	Kasganj	Mohanpur (NP)	5	Operational	
77	Kasganj	Patiyali (NP)	5	Operational	
78	Kasganj	Sahawar (NP)	5	Operational	
79	Kasganj	Sidhpura (NP)	5	Operational	
80	Kasganj	Soron (NPP)	5	Operational	
81	Ambedkar Nagar	Ilitfatganj (NP)	5	Operational	
82	Amethi	Gauriganj (NPP)	5	Operational	
83	Amethi	Musafirkhana (NP)	5	Operational	
84	Ayodhya	Ayodhya (M Corp.)	5	Operational	
85	Ayodhya	Bikapur (NP)	5	Operational	
86	Barabanki	Banki (NP)	5	Operational	
87	Barabanki	Belhara (NP)	5	Operational	
88	Barabanki	Dariyabad (NP)	5	Operational	
89	Barabanki	Dewa (NP)	5	Operational	
90	Barabanki	Fatehpur (NP)	5	Operational	
91	Barabanki	Haidergarh (NP)	5	Operational	
92	Barabanki	Nawabganj (NPP)	5	Operational	
93	Barabanki	Ramnagar (NP)	5	Operational	
94	Barabanki	Satrikh (NP)	5	Operational	
95	Barabanki	Siddhaur (NP)	5	Operational	
96	Barabanki	Tikait Nagar (NP)	5	Operational	
97	Barabanki	Zaidpur (NP)	5	Operational	
98	Sultanpur	Dostpur (NP)	5	Operational	
99	Sultanpur	Kadipur (NP)	5	Operational	
100	Sultanpur	Koeripur (NP)	5	Operational	
101	Sultanpur	Sultanpur (NPP)	5	Operational	
102	Azamgarh	Atrauliya (NP)	5	Operational	
103	Azamgarh	Bilariaganj (NP)	5	Operational	
104	Azamgarh	Jiyanpur (NP)	5	Operational	
105	Azamgarh	Katghar Lalganj (NP)	5	Operational	
106	Azamgarh	Mahraiganj (NP)	5	Operational	
107	Azamgarh	Mahul (NP)	5	Operational	
108	Azamgarh	Mehnagar (NP)	5	Operational	
109	Azamgarh	Mubarakpur (NPP)	5	Operational	
110	Azamgarh	Nizamabad (NP)	5	Operational	
111	Azamgarh	Sarai Mir (NP)	5	Operational	
112	Ballia	Belthara Road (NP)	5	Operational	
113	Ballia	Rasra (NPP)	5	Operational	
114	Ballia	Reoti (NP)	5	Operational	
115	Ballia	Sikanderpur (NP)	5	Operational	
116	Mau	Kopaganj (NP)	5	Operational	
117	Badaun	Allapur (NP)	5	Operational	
118	Badaun	Bilsi (NPP)	5	Operational	
119	Badaun	Bisauli (NPP)	5	Operational	
120	Badaun	Budaun (NPP)	5	Operational	
121	Badaun	Dataganj (NPP)	5	Operational	
122	Badaun	Faizganj (NP)	5	Operational	
123	Badaun	Gulariya (NP)	5	Operational	
124	Badaun	Islamnagar (NP)	5	Operational	
125	Badaun	Kachhla (NP)	5	Operational	
126	Badaun	Kakralla (NPP)	5	Operational	
127	Badaun	Kunwargaon (NP)	5	Operational	
128	Badaun	Mundiya (NP)	5	Operational	
129	Badaun	Rudayan (NP)	5	Operational	
130	Badaun	Sahaswan (NPP)	5	Operational	
131	Badaun	Saidpur (NP)	5	Operational	
132	Badaun	Sakhanu (NP)	5	Operational	
133	Badaun	Ujhani (NPP)	5	Operational	
134	Badaun	Usawan (NP)	5	Operational	
135	Badaun	Usehat (NP)	5	Operational	
136	Badaun	Wazirganj (NP)	5	Operational	

137	Bareilly	Aonla (NPP)	5	Operational	
138	Bareilly	Baheri (NPP)	5	Operational	
139	Bareilly	Bareilly (M Corp.)	5	Operational	
140	Bareilly	Bisharatganj (NP)	5	Operational	
141	Bareilly	Deoranian (NP)	5	Operational	
142	Bareilly	Dhaura Tanda (NP)	5	Operational	
143	Bareilly	Faridpur (NP)	5	Operational	
144	Bareilly	Faridpur (NPP)	5	Operational	
145	Bareilly	Fatehganj Pashchimi (NP)	5	Operational	
146	Bareilly	Fatehganj Purvi (NP)	5	Operational	
147	Bareilly	Mirganj (NP)	5	Operational	
148	Bareilly	Richha (NP)	5	Operational	
149	Bareilly	Rithora (NP)	5	Operational	
150	Bareilly	Sainthal (NP)	5	Operational	
151	Bareilly	Shahi (NP)	5	Operational	
152	Bareilly	Shergarh (NP)	5	Operational	
153	Bareilly	Shishgarh (NP)	5	Operational	
154	Bareilly	Sirauli (NP)	5	Operational	
155	Bareilly	Thirya Nizawat Khan (NP)	5	Operational	
156	Pilibhit	Barkhera (NP)	5	Operational	
157	Pilibhit	Bilsanda (NP)	5	Operational	
158	Pilibhit	Bisalpur (NPP)	5	Operational	
159	Pilibhit	Gulariya Bhindara (NP)	5	Operational	
160	Pilibhit	Jahanabad (NP)	5	Operational	
161	Pilibhit	Kalinagar (NP)	5	Operational	
162	Pilibhit	Nyoria Husainpur (NP)	5	Operational	
163	Pilibhit	Pilibhit (NPP)	5	Operational	
164	Pilibhit	Puranpur (NPP)	5	Operational	
165	Shahjahanpur	Allahganj (NP)	5	Operational	
166	Shahjahanpur	Jalalabad (NPP)	5	Operational	
167	Shahjahanpur	Kanth (NP)	5	Operational	
168	Shahjahanpur	Katra (NP)	5	Operational	
169	Shahjahanpur	Khudaganj (NP)	5	Operational	
170	Shahjahanpur	Khutar (NP)	5	Operational	
171	Shahjahanpur	Powayan (NPP)	5	Operational	
172	Shahjahanpur	Shahjahanpur (M Corp.)	5	Operational	
173	Shahjahanpur	Tilhar (NPP)	5	Operational	
174	Basti	Basti (NPP)	5	Operational	
175	Basti	Harraiya (NP)	5	Operational	
176	Basti	Rudhauri Bazar (NP)	5	Operational	
177	Sant Kabir Nagar	Hariharpur (NP)	5	Operational	
178	Sant Kabir Nagar	Khalilabad (NPP)	5	Operational	
179	Sant Kabir Nagar	Maghar (NP)	5	Operational	
180	Sant Kabir Nagar	Mehdawal (NP)	5	Operational	
181	Siddharth Nagar	Bansi (NPP)	5	Operational	
182	Siddharth Nagar	Barhani Bazar (NP)	5	Operational	
183	Banda	Banda (NPP)	5	Operational	
184	Banda	Atarra (NPP)	5	Operational	
185	Banda	Baberu (NP)	5	Operational	
186	Banda	Bisanda Buzurg (NP)	5	Operational	
187	Banda	Mataundh (NP)	5	Operational	
188	Banda	Naraini (NP)	5	Operational	
189	Banda	Oran (NP)	5	Operational	
190	Banda	Tindwari (NP)	5	Operational	
191	Chitrakoot	Manikpur Sarhat (NP)	5	Operational	
192	Hamirpur	Hamirpur (NPP)	5	Operational	
193	Hamirpur	Maudaha (NPP)	5	Operational	
194	Hamirpur	Rath (NPP)	5	Operational	
195	Hamirpur	Sarila (NP)	5	Operational	
196	Mahoba	Charkhari (NPP)	5	Operational	
197	Mahoba	Kabrai (NP)	5	Operational	
198	Mahoba	Kharela (NP)	5	Operational	
199	Mahoba	Kul Pahar (NP)	5	Operational	
200	Mahoba	Mahoba (NPP)	5	Operational	
201	Bahraich	Bahraich (NPP)	5	Operational	
202	Balrampur	Pachperwa (NP)	5	Operational	
203	Balrampur	Tulsipur (NP)	5	Operational	

204	Gonda	Katra (NP)	5	Operational	
205	Gonda	Paraspur (NP)	5	Operational	
206	Sravasti	Bhinga (NPP)	5	Operational	
207	Sravasti	Ikauna (NP)	5	Operational	
208	Deoria	Bariyarpur (NP)	5	Operational	
209	Deoria	Bhatpar Rani (NP)	5	Operational	
210	Deoria	Deoria (NPP)	5	Operational	
211	Deoria	Gaura Barhaj (NPP)	5	Operational	
212	Deoria	Gauri Bazar (NP)	5	Operational	
213	Deoria	Lar (NP)	5	Operational	
214	Deoria	Majhauriraj (NP)	5	Operational	
215	Deoria	Rampur Karkhana (NP)	5	Operational	
216	Deoria	Rudrapur (NP)	5	Operational	
217	Deoria	Salempur (NP)	5	Operational	
218	Gorakhpur	Gola Bazar (NP)	5	Operational	
219	Gorakhpur	Gorakhpur (M Corp.)	5	Operational	
220	Gorakhpur	Pipraich (NP)	5	Operational	
221	Gorakhpur	Sahjanwan (NP)	5	Operational	
222	Kushinagar	Hata (NPP)	5	Operational	
223	Kushinagar	Kaptanganj (NP)	5	Operational	
224	Maharajganj	Anandnagar (NP)	5	Operational	
225	Maharajganj	Maharajganj (NPP)	5	Operational	
226	Maharajganj	Nautanwa (NPP)	5	Operational	
227	Maharajganj	Nichlaul (NP)	5	Operational	
228	Maharajganj	Siswa Bazar (NP)	5	Operational	
229	Maharajganj	Sonauli (NP)	5	Operational	
230	Jalaun	AIT (NP)	5	Operational	
231	Jalaun	Jalaun (NPP)	5	Operational	
232	Jalaun	Kadavra (NP)	5	Operational	
233	Jalaun	Kalpi (NPP)	5	Operational	
234	Jalaun	Konch (NPP)	5	Operational	
235	Jalaun	Kotra (NP)	5	Operational	
236	Jalaun	Madhogarh (NP)	5	Operational	
237	Jalaun	Nadigaon (NP)	5	Operational	
238	Jalaun	Orai (NPP)	5	Operational	
239	Jalaun	Rampura (NP)	5	Operational	
240	Jalaun	Umri (NP)	5	Operational	
241	Jaunpur	Jaunpur (NPP)	5	Operational	
242	Jhansi	Baragaon (NP)	5	Operational	
243	Jhansi	Barua Sagar (NPP)	5	Operational	
244	Jhansi	Chirgaon (NPP)	5	Operational	
245	Jhansi	Erich (NP)	5	Operational	
246	Jhansi	Garautha (NP)	5	Operational	
247	Jhansi	Gursarai (NPP)	5	Operational	
248	Jhansi	Jhansi (M Corp.)	5	Operational	
249	Jhansi	Kathera (NP)	5	Operational	
250	Jhansi	Mauranipur (NPP)	5	Operational	
251	Jhansi	Moth (NP)	5	Operational	
252	Jhansi	Ranipur (NP)	5	Operational	
253	Jhansi	Samthar (NPP)	5	Operational	
254	Jhansi	Tondi Fatehpur (NP)	5	Operational	
255	Lalitpur	Lalitpur (NPP)	5	Operational	
256	Lalitpur	Mahroni (NP)	5	Operational	
257	Lalitpur	Pali (NP)	5	Operational	
258	Lalitpur	Talbehat (NP)	5	Operational	
259	Auraiya	Achhalda (NP)	5	Operational	
260	Auraiya	Atasu (NP)	5	Operational	
261	Auraiya	Auraiya (NPP)	5	Operational	
262	Auraiya	Babarpur Ajitmal (NP)	5	Operational	
263	Auraiya	Bidhuna (NP)	5	Operational	
264	Auraiya	Dibiyapur (NP)	5	Operational	
265	Auraiya	Phaphund (NP)	5	Operational	
266	Etawah	Bharthana (NPP)	5	Operational	
267	Etawah	Ekdil (NP)	5	Operational	
268	Etawah	Etawah (NPP)	5	Operational	
269	Etawah	Jaswantnagar (NPP)	5	Operational	
270	Farrukhabad	Farrukhabad (NPP) (G)	5	Operational	
271	Farrukhabad	Kaimganj (NPP)	5	Operational	
272	Farrukhabad	Kamalganj (NP)	5	Operational	
273	Farrukhabad	Kampil (NP)	5	Operational	
274	Farrukhabad	Mohammadabad (NP)	5	Operational	

275	Farrukhabad	Shamsabad (NP)	5	Operational	
276	Kannauj	Chhibramau (NPP)	5	Operational	
277	Kannauj	Gursahaiganj (NPP)	5	Operational	
278	Kannauj	Samdhan (NP)	5	Operational	
279	Kannauj	Sikanderpur (NP)	5	Operational	
280	Kannauj	Talgram (NP)	5	Operational	
281	Kannauj	Tirwaganj (NP)	5	Operational	
282	Kanpur Dehat	Akbarpur (NP)	5	Operational	
283	Kanpur Dehat	Derapur (NP)	5	Operational	
284	Kanpur Dehat	Jhinhak (NPP)	5	Operational	
285	Kanpur Dehat	Pukhrayan (NPP)	5	Operational	
286	Kanpur Dehat	Rasulabad (NP)	5	Operational	
287	Kanpur Dehat	Rura (NP)	5	Operational	
288	Kanpur Dehat	Shivli (NP)	5	Operational	
289	Kanpur Dehat	Sikandra (NP)	5	Operational	
290	Kanpur Nagar	Kanpur (M Corp.) (G)	5	Operational	
291	Kanpur Nagar	Shivrajpur (NP)	5	Operational	
292	Hardoi	Beniganj (NP)	5	Operational	
293	Hardoi	Bilgram (NPP)	5	Operational	
294	Hardoi	Gopamau (NP)	5	Operational	
295	Hardoi	Hardoi (NPP)	5	Operational	
296	Hardoi	Madhoganj (NP)	5	Operational	
297	Hardoi	Mallawan (NPP)	5	Operational	
298	Hardoi	Pali (NP)	5	Operational	
299	Hardoi	Pihani (NPP)	5	Operational	
300	Hardoi	Sandila (NPP)	5	Operational	
301	Hardoi	Shahabad (NPP)	5	Operational	
302	Kheeri	Barwar (NP)	5	Operational	
303	Kheeri	Dhaurehra (NP)	5	Operational	
304	Kheeri	Gola Gokarannath (NPP)	5	Operational	
305	Kheeri	Kheri (NP)	5	Operational	
306	Kheeri	Lakhimpur (NPP)	5	Operational	
307	Kheeri	Mailani (NP)	5	Operational	
308	Kheeri	Mohammadi (NPP)	5	Operational	
309	Kheeri	Oel Dhakwa (NP)	5	Operational	
310	Kheeri	Paliya Kalan (NPP)	5	Operational	
311	Kheeri	Singahi Bhindaura (NP)	5	Operational	
312	Lucknow	Amethi (NP)	5	Operational	
313	Lucknow	Bakshi Ka Talab (NP)	5	Operational	
314	Lucknow	Gosainganj (NP)	5	Operational	
315	Lucknow	Itaunja (NP)	5	Operational	
316	Lucknow	Kakori (NP)	5	Operational	
317	Lucknow	Lucknow (M Corp.)	5	Operational	
318	Lucknow	Mahona (NP)	5	Operational	
319	Lucknow	Nagram (NP)	5	Operational	
320	Raebareilly	Bachhrawan (NP)	5	Operational	
321	Raebareilly	Dalmau (NP)	5	Operational	
322	Raebareilly	Maharajganj (NP)	5	Operational	
323	Raebareilly	Nasirabad (NP)	5	Operational	
324	Raebareilly	Parsadepur (NP)	5	Operational	
325	Raebareilly	Salon (NP)	5	Operational	
326	Raebareilly	Unchahar (NP)	5	Operational	
327	Sitapur	Biswan (NPP)	5	Operational	
328	Sitapur	Hargaon (NP)	5	Operational	
329	Sitapur	Khairabad (NPP)	5	Operational	
330	Sitapur	Laharpur (NPP)	5	Operational	
331	Sitapur	Mahmudabad (NPP)	5	Operational	
332	Sitapur	Maholi (NP)	5	Operational	
333	Sitapur	Misrikh-Naimish (NPP)	5	Operational	
334	Sitapur	Paintepur (NP)	5	Operational	
335	Sitapur	Sidhauli (NP)	5	Operational	
336	Sitapur	Sitapur (NPP)	5	Operational	
337	Sitapur	Tambaur- Ahamdabad (NP)	5	Operational	
338	Unnao	Auras (NP)	5	Operational	
339	Unnao	Bangarmau (NPP)	5	Operational	
340	Unnao	Bhagwant Nagar (NP)	5	Operational	
341	Unnao	Bighapur (NP)	5	Operational	
342	Unnao	Fatehpur Chaurasi (NP)	5	Operational	
343	Unnao	Gangaghat (NPP) (G)	5	Operational	
344	Unnao	Ganj Muradabad (NP)	5	Operational	

345	Unnao	Hyderabad (NP)	5	Operational	
346	Unnao	Kursath (NP)	5	Operational	
347	Unnao	Maurawan (NP)	5	Operational	
348	Unnao	Mohan (NP)	5	Operational	
349	Unnao	Nawabganj (NP)	5	Operational	
350	Unnao	Nyotini (NP)	5	Operational	
351	Unnao	Purwa (NP)	5	Operational	
352	Unnao	Rasulabad (NP)	5	Operational	
353	Unnao	Safipur (NP)	5	Operational	
354	Unnao	Ugu (NP)	5	Operational	
355	Unnao	Unnao (NPP)	5	Operational	
356	Bagpat	Aminagar Sarai (NP)	5	Operational	
357	Bagpat	Baraut (NPP)	5	Operational	
358	Bagpat	Chhaprauli (NP)	5	Operational	
359	Bagpat	Doghat (NP)	5	Operational	
360	Bagpat	Khekada (NPP)	5	Operational	
361	Bagpat	Tikri (NP)	5	Operational	
362	Bulandsahar	Anupshahr (NPP) (G)	5	Operational	
363	Bulandsahar	Aurangabad (NP)	5	Operational	
364	Bulandsahar	Bhawan Bahadurnagar (NP)	5	Operational	
365	Bulandsahar	Bugrasi (NP)	5	Operational	
366	Bulandsahar	Chhatari (NP)	5	Operational	
367	Bulandsahar	Dibai (NPP)	5	Operational	
368	Bulandsahar	Gulaoti (NPP)	5	Operational	
369	Bulandsahar	Jahangirabad (NPP)	5	Operational	
370	Bulandsahar	Khanpur (NP)	5	Operational	
371	Bulandsahar	Khurja (NPP)	5	Operational	
372	Bulandsahar	Naraura (NP) (G)	5	Operational	
373	Bulandsahar	Shikarpur (NPP)	5	Operational	
374	Bulandsahar	Siana (NPP)	5	Operational	
375	Bulandsahar	Sikandrabad (NPP)	5	Operational	
376	Gautam Buddh Nagar	Bilaspur (NP)	5	Operational	
377	Gautam Buddh Nagar	Dadri (NPP)	5	Operational	
378	Gautam Buddh Nagar	Jewar (NP)	5	Operational	
379	Ghaziabad	Faridnagar (NP)	5	Operational	
380	Ghaziabad	Ghaziabad (M Corp.)	5	Operational	
381	Ghaziabad	Modinagar (NPP)	5	Operational	
382	Ghaziabad	Niwari (NP)	5	Operational	
383	Hapur	Garhmukhteshwar (NPP)(G)	5	Operational	
384	Hapur	Hapur (NPP)	5	Operational	
385	Meerut	Daurala (NP)	5	Operational	
386	Meerut	Harra (NP)	5	Operational	
387	Meerut	Hastinapur (NP) (G)	5	Operational	
388	Meerut	Karnawal (NP)	5	Operational	
389	Meerut	Kharkhauda (NP)	5	Operational	
390	Meerut	Khiwai (NP)	5	Operational	
391	Meerut	Lawar (NP)	5	Operational	
392	Meerut	Mawana (NPP)	5	Operational	
393	Meerut	Parikshitgarh (NP)	5	Operational	
394	Meerut	Phalauda (NP)	5	Operational	
395	Meerut	Sardhana (NPP)	5	Operational	
396	Meerut	Sewalkhas (NP)	5	Operational	
397	Meerut	Shahjahanpur (NP)	5	Operational	
398	Bhadohi	Bhadohi (NPP)	5	Operational	
399	Bhadohi	Ghosia Bazar (NP)	5	Operational	
400	Bhadohi	Gopiganj (NPP)	5	Operational	
401	Bhadohi	Gyanpur (NP)	5	Operational	
402	Bhadohi	Khamaria (NP)	5	Operational	
403	Bhadohi	Nai Bazar (NP)	5	Operational	
404	Bhadohi	Suriyawan (NP)	5	Operational	
405	Mirzapur	Ahaura (NPP)	5	Operational	
406	Mirzapur	Chunar (NPP) (G)	5	Operational	
407	Mirzapur	Mirzapur (NPP) (G)	5	Operational	
408	Sonbhadra	Chopan (NP)	5	Operational	
409	Sonbhadra	Dudhi (NP)	5	Operational	
410	Sonbhadra	Ghorawal (NP)	5	Operational	

411	Sonbhadra	Pipri (NP)	5	Operational	
412	Sonbhadra	Renukoot (NP)	5	Operational	
413	Sonbhadra	Sonbhadra- Robertsganj (NPP)	5	Operational	
414	Amroha	Amroha (NPP)	5	Operational	
415	Amroha	Bachhraon (NPP)	5	Operational	
416	Amroha	Dhanaura (NPP)	5	Operational	
417	Amroha	Gajraula (NPP)	5	Operational	
418	Amroha	Hasanpur (NPP)	5	Operational	
419	Amroha	Joya (NP)	5	Operational	
420	Amroha	Naugawan Sadat (NP)	5	Operational	
421	Amroha	Ujhari (NP)	5	Operational	
422	Bijnor	Afzalgarh (NPP)	5	Operational	
423	Bijnor	Bijnore (NPP) (G)	5	Operational	
424	Bijnor	Chandpur (NPP)	5	Operational	
425	Bijnor	Dhampur (NPP)	5	Operational	
426	Bijnor	Haldaur (NPP)	5	Operational	
427	Bijnor	Jalalabad (NP)	5	Operational	
428	Bijnor	Jhalu (NP)	5	Operational	
429	Bijnor	Kiratpur (NPP)	5	Operational	
430	Bijnor	Mandawar (NP)	5	Operational	
431	Bijnor	Nagina (NPP)	5	Operational	
432	Bijnor	Najibabad (NPP)	5	Operational	
433	Bijnor	Nehtaur (NPP)	5	Operational	
434	Bijnor	Noorpur (NPP)	5	Operational	
435	Bijnor	Sahanpur (NP)	5	Operational	
436	Bijnor	Sahaspur (NP)	5	Operational	
437	Bijnor	Seohara (NPP)	5	Operational	
438	Bijnor	Sherkot (NPP)	5	Operational	
439	Bijnor	Warhapur (NP)	5	Operational	
440	Moradabad	Agwanpur (NP)	5	Operational	
441	Moradabad	Bhojpur Dharampur (NP)	5	Operational	
442	Moradabad	Bilari (NPP)	5	Operational	
443	Moradabad	Kanth (NP)	5	Operational	
444	Moradabad	Kundarki (NP)	5	Operational	
445	Moradabad	Moradabad (M Corp.)	5	Operational	
446	Moradabad	Pakbada (NP)	5	Operational	
447	Moradabad	Thakurdwara (NPP)	5	Operational	
448	Moradabad	Umri Kalan (NP)	5	Operational	
449	Rampur	Bilaspur (NPP)	5	Operational	
450	Rampur	Maswasi (NP)	5	Operational	
451	Rampur	Milak (NPP)	5	Operational	
452	Rampur	Rampur (NPP)	5	Operational	
453	Rampur	Swar (NPP)	5	Operational	
454	Rampur	Tanda (NPP)	5	Operational	
455	Sambhal	Bahjoi (NPP)	5	Operational	
456	Sambhal	Chandausi (NPP)	5	Operational	
457	Sambhal	Gawan (NP)	5	Operational	
458	Sambhal	Gunnaur (NP)	5	Operational	
459	Sambhal	Narauli (NP)	5	Operational	
460	Sambhal	Sambhal (NPP)	5	Operational	
461	Sambhal	Sirsi (NP)	5	Operational	
462	Fatehpur	ASOTHER (NP)	5	Operational	
463	Fatehpur	Bindki (NPP)	5	Operational	
464	Fatehpur	Fatehpur (NPP)	5	Operational	
465	Fatehpur	Hathgaam (NP)	5	Operational	
466	Fatehpur	Khaga (NP)	5	Operational	
467	Fatehpur	Kora Jahanabad (NP)	5	Operational	
468	Kaushambi	Ajhuwa (NP)	5	Operational	
469	Kaushambi	Bharwari (NP)	5	Operational	
470	Kaushambi	Chail (NP)	5	Operational	
471	Kaushambi	Karari (NP)	5	Operational	
472	Kaushambi	Manjhanpur (NP)	5	Operational	
473	Kaushambi	Sarai Aquil (NP)	5	Operational	
474	Kaushambi	Sirathu (NP)	5	Operational	
475	Pratapgarh	Bela Pratapgarh (NPP)	5	Operational	
476	Pratapgarh	Katra Medniganj (NP)	5	Operational	
477	Pratapgarh	Kunda (NP)	5	Operational	
478	Pratapgarh	Lalganj (NP)	5	Operational	
479	Pratapgarh	Manikpur (NP)	5	Operational	
480	Pratapgarh	Patti (NP)	5	Operational	

481	Pratapgarh	Pratapgarh City (NP)	5	Operational	
482	Pratapgarh	Raniganj (NP)	5	Operational	
483	Prayagraj	Bharatganj (NP)	5	Operational	
484	Prayagraj	Handia (NP)	5	Operational	
485	Prayagraj	Koraon (NP)	5	Operational	
486	Prayagraj	Lal Gopalganj (NP)	5	Operational	
487	Prayagraj	Mau Aima (NP)	5	Operational	
488	Prayagraj	Phulpur (NP)	5	Operational	
489	Prayagraj	Prayagraj (M Corp.) (G)	10	Operational	
490	Prayagraj	Prayagraj (M Corp.) (G) (Jhusi)	10	Operational	
491	Prayagraj	Shankargarh (NP)	5	Operational	
492	Prayagraj	Sirsa (NP)	5	Operational	
493	Muzaffarnagar	Bhokarhedi (NP)	5	Operational	
494	Muzaffarnagar	Budhana (NP)	5	Operational	
495	Muzaffarnagar	Charthawal (NP)	5	Operational	
496	Muzaffarnagar	Jansath (NP)	5	Operational	
497	Muzaffarnagar	Khatauli (NPP)	5	Operational	
498	Muzaffarnagar	Mirapur (NP)	5	Operational	
499	Muzaffarnagar	Purquazi (NP)	5	Operational	
500	Muzaffarnagar	Shahpur (NP)	5	Operational	
501	Saharanpur	Ambehta (NP)	5	Operational	
502	Saharanpur	Behat (NP)	5	Operational	
503	Saharanpur	Chilkana Sultanpur (NP)	5	Operational	
504	Saharanpur	Deoband (NPP)	5	Operational	
505	Saharanpur	Gangoh (NPP)	5	Operational	
506	Saharanpur	Nakur (NPP)	5	Operational	
507	Saharanpur	Nanauta (NP)	5	Operational	
508	Saharanpur	Rampur Maniharan (NP)	5	Operational	
509	Saharanpur	Saharanpur (M Corp.)	5	Operational	
510	Saharanpur	Sarsawa (NPP)	5	Operational	
511	Saharanpur	Titron (NP)	5	Operational	
512	Shamli	Ailam (NP)	5	Operational	
513	Shamli	Banat (NP)	5	Operational	
514	Shamli	Garhi Pukhta (NP)	5	Operational	
515	Shamli	Jalalabad (NP)	5	Operational	
516	Shamli	Jhinjhana (NP)	5	Operational	
517	Shamli	Kairana (NPP)	5	Operational	
518	Shamli	Kandhla (NPP)	5	Operational	
519	Shamli	Shamli (NPP)	5	Operational	
520	Shamli	Un (NP)	5	Operational	
521	Chandauli	Chakia (NP)	5	Operational	
522	Chandauli	Chandauli (NP)	5	Operational	
523	Chandauli	Mughalsarai (NPP)(G)	5	Operational	
524	Chandauli	Saiyad Raza (NP)	5	Operational	
525	Ghazipur	Bahadurganj (NP)	5	Operational	
526	Ghazipur	Dildarnagar (NP)	5	Operational	
527	Ghazipur	Ghazipur (NPP) (G)	5	Operational	
528	Ghazipur	Jangipur (NP)	5	Operational	
529	Ghazipur	Mohammadabad (NPP)	5	Operational	
530	Ghazipur	Sadat (NP)	5	Operational	
531	Ghazipur	Saidpur (NP) (G)	5	Operational	
532	Jaunpur	Kerakat (NP)	5	Operational	
533	Jaunpur	Khetasarai (NP)	5	Operational	
534	Jaunpur	Mariahu (NP)	5	Operational	
535	Varanasi	Gangapur (NP)	5	Operational	
TOTAL			2685		

Solid Waste Progress Report						
Current Status						
161 ULBs(Compost Pits)						
S.No.	District	ULB Name	No. Of Pit	Pit Composting Capacity (TPD)	Pit Composting Utilized (TPD)	Issues related to progress
1	Agra	Agra	44	528	528	No issue
2	Agra	Shamsabad	5	6.5	2.5	No issue
3	Agra	Fatehpur Sikri	5	6.5	2.5	No issue
4	Agra	ACHHNERA	4	4	2	No issue
5	Agra	ETMADPUR	4	4	2	No issue
6	Agra	Bah	2	2.8	1.5	No issue
7	Agra	Jagner	2	2	1	No issue
8	Agra	Kheragarh	4	4.5	1.8	No issue
9	Agra	Kiraoli	4	4.5	1	No issue
10	Agra	Pinahat	3	3	1	No issue
11	Amroha	Hasanpur	6	7.5	7	No issue
12	Amroha	Bachhraon	5	2	1	No issue
13	Amroha	Naugawan Sadat	6	4	6	No issue
14	Bareilly	Bisharatganj	2	5	5	No issue
15	Bareilly	Fatehganj Pashchimi	2	5	5	No issue
16	Bareilly	Meerganj	2	5	1.99	No issue
17	Basti	Basti	2	2	2	No issue
18	Bhadohi	Bhadohi	2	4	2	No issue
19	Bhadohi	Nai Bazar	3	3	1	No issue
20	Bhadohi	Gopiganj	2	1.5	0.5	No issue
21	Bulandshahr	Anupshahr	5	0.5	0.5	No issue
22	Etah	Etah	3	5	5	No issue
23	Etah	Marhera	4	5	5	No issue
24	Etah	Aliganj	4	5	5	No issue
25	Etah	Awagarh	2	4	2.3	No issue
26	Etah	Jaithara	1	5	2.52	No issue
27	Etah	Nidhauri Kalan	2	2	1.77	No issue
28	Etah	Sakit	2	2	1.69	No issue
29	Etawah	Etawah	5	5	5	No issue
30	Etawah	Bharthana	3	3	3	No issue
31	Etawah	Jaswantnagar	3	3	3	No issue
32	Etawah	Bakewar	1	1	1	No issue
33	Etawah	Ekdil	2	2	2	No issue
34	Etawah	Lakhna	1	1	1	No issue
35	Farrukhabad	Farrukhabad	3	3	3	No issue
36	Farrukhabad	Kaimganj	8	4	4	No issue
37	Farrukhabad	Kamalganj	1	1	1	No issue
38	Farrukhabad	Kampil	1	1	1	No issue
39	Farrukhabad	Mohammadabad	6	4	4	No issue
40	Farrukhabad	Shamsabad	10	5	5	No issue

41	Fatehpur	Fatehpur	5	20	20	No issue
42	Fatehpur	Bindki	4	8	4	No issue
43	Fatehpur	Hathgam	1	1	1	No issue
44	Fatehpur	Khaga	67	30	30	No issue
45	Fatehpur	Kora Jahanabad	6	12	3	No issue
46	Hamirpur	Gohand	3	3	2	No issue
47	Hardoi	Hardoi	4	12	12	No issue
48	Hardoi	Shahabad	2	3	3	No issue
49	Hardoi	Sandila	4	5.5	5.5	No issue
50	Hardoi	Mallawan	4	3	3	No issue
51	Hardoi	PIHANI	2	4.5	4.5	No issue
52	Hardoi	Bilgram	6	4	4	No issue
53	Hardoi	Sandi	2	3.5	3.5	No issue
54	Hardoi	Beniganj	2	1.5	1.5	No issue
55	Hardoi	Gopamau	4	2.23	2.23	No issue
56	Hardoi	Kachhauna Patseni	2	2.1	2.1	No issue
57	Hardoi	Kursath	2	0.1	0.1	No issue
58	Hardoi	Madhoganj	2	4	4	No issue
59	Hardoi	Pali	2	2.35	2.35	No issue
60	Hathras	Hathras	8	8	6	No issue
61	Hathras	Sadabad	8	8	4	No issue
62	Kaushambi	Bharwari	5	5	1	No issue
63	Kaushambi	Manjhanpur	8	8	1	No issue
64	Kaushambi	Ajhuwa	2	2	0.5	No issue
65	Kaushambi	Chail	1	1	0.25	No issue
66	Kaushambi	Karari	2	2	0.5	No issue
67	Kaushambi	Daranagar	2	2	0.5	No issue
68	Kaushambi	Purab Pashchim Sharira	2	2	0.5	No issue
69	Kaushambi	Sarai Aquil	2	2	0.5	No issue
70	Kaushambi	Sirathu	2	2	0.5	No issue
71	Kaushambi	Charwa	2	2	0.5	No issue
72	Kushinagar	Padrauna	2	2	2	No issue
73	Kushinagar	Kushinagar	2	5	2	No issue
74	Kushinagar	Hata	2	5	2	No issue
75	Kushinagar	Kaptanganj	1	2	2	No issue
76	Kushinagar	Dudahi	2	2	2	No issue
77	Kushinagar	Ramkola	1	2	2	No issue
78	Kushinagar	Sewarhi	1	1	1	No issue
79	Lakimpur Kheri	Lakhimpur	5	5	5	No issue
80	Lakimpur Kheri	Gola Gokarannath	1	1	1	No issue
81	Lakimpur Kheri	MOHAMMADI	1	1	1	No issue
82	Lakimpur Kheri	Barwar	16	16	3	No issue
83	Lakimpur Kheri	Dhaurahra	4	10	6	No issue
84	Lakimpur Kheri	Kheri	2	2	2	No issue

85	Lakimpur Kheri	Mailani	1	1	1	No issue
86	Lakimpur Kheri	Oel Dhakhwa	2	1	2	No issue
87	Lakimpur Kheri	Singahi Bhedaura	1	1	1	No issue
88	Lucknow	Lucknow	142	213	213	No issue
89	Lucknow	Amethi	2	6	6	No issue
90	Lucknow	Bakshi Ka Talab	2	6	6	No issue
91	Lucknow	Gosaiganj	1	3	3	No issue
92	Lucknow	Itaunja	1	3	3	No issue
93	Lucknow	Kakori	1	3	3	No issue
94	Lucknow	Mahona	1	3	3	No issue
95	Lucknow	Malihabad	1	3	3	No issue
96	Lucknow	Banthara	2	6	6	No issue
97	Lucknow	Mohanlalganj	2	6	6	No issue
98	Lucknow	Nagram	2	6	6	No issue
99	Mahoba	Mahoba	6	2	3.25	No issue
100	Mahoba	Charkhari	3	1	1	No issue
101	Mahoba	Kabrai	3	1	1	No issue
102	Mahoba	Kharela	3	1	1	No issue
103	Mahoba	Kulpahar	6	2	2	No issue
104	Mainpuri	Mainpuri	18	30	30	No issue
105	Meerut	Shahjahanpur	1	4	2.37	No issue
106	Meerut	Siwalkhas	1	2	0.5	No issue
107	Mirzapur	Mirzapur	2	2	2	No issue
108	Mirzapur	Chunar	2	3	3	No issue
109	Mirzapur	Ahraura	1	0.5	0.5	No issue
110	Mirzapur	Kachhwa	2	1	1	No issue
111	Muzaffarnagar	Muzaffarnagar	3	3	3	No issue
112	Muzaffarnagar	Khatauli	3	3	3	No issue
113	Muzaffarnagar	Bhokerheri	3	3	3	No issue
114	Muzaffarnagar	Budhana	3	3	3	No issue
115	Muzaffarnagar	Charthawal	3	3	3	No issue
116	Muzaffarnagar	Jansath	3	3	3	No issue
117	Muzaffarnagar	Meerapur	3	3	3	No issue
118	Muzaffarnagar	Purquazi	3	3	3	No issue
119	Muzaffarnagar	Shahpur	3	3	3	No issue
120	Muzaffarnagar	Sisauli	3	3	3	No issue
121	Pilibhit	Neoria Husainpur	1	10	3.6	No issue
122	Pratapgarh	Pratapgarh	5	10	10	No issue
123	Rae Bareli	Rae Bareli	7	12	12	No issue
124	Rae Bareli	Bachhrawan	2	2	2	No issue
125	Rae Bareli	Dalmau	1	1	1	No issue
126	Rae Bareli	Lalganj	2	2	2	No issue
127	Rae Bareli	Maharajganj	1	1	1	No issue
128	Rae Bareli	Nasirabad	2	2	2	No issue
129	Rae Bareli	Parshadepur	1	1	1	No issue
130	Rae Bareli	Salon	2	2	2	No issue
131	Rae Bareli	Unchahar	1	1	1	No issue

132	Saharanpur	Saharanpur	20	35	35	No issue
133	Saharanpur	Deoband	3	15	15	No issue
134	Sambhal	Chandausi	10	3	3	No issue
135	Sambhal	Babrala	6	2	2	No issue
136	Sambhal	Sirsi	30	6	5.6	No issue
137	Shahjahanpur	Powayan	4	4	4	No issue
138	Shahjahanpur	Allahganj	2	2	2	No issue
139	Shahjahanpur	Katra	2	2	2	No issue
140	Shahjahanpur	Khutar	5	5	5	No issue
141	Shahjahanpur	Banda	1	1	1	No issue
142	Shamli	Shamli	10	5	5	No issue
143	Shravasti	Ikauna	6	1	0.5	No issue
144	Sitapur	Sitapur	10	10	10	No issue
145	Sitapur	Mahmudabad	5	5	5	No issue
146	Sitapur	Laharpur	8	8	8	No issue
147	Sitapur	Biswan	10	10	10	No issue
148	Sitapur	KHAIRABAD	40	20	16	No issue
149	Sitapur	Mishritnaimishar nya	2	2	2	No issue
150	Sitapur	Hargaon	6	5	5	No issue
151	Sitapur	Maholi	5	5	5	No issue
152	Sitapur	Paintepur	4	4	4	No issue
153	Sitapur	Sidhauri	8	8	8	No issue
154	Sitapur	Tambaur Cum Ahmadabad	8	5	5	No issue
155	Sonbhadra	Robertsganj (sonbhadra)	2	5	5	No issue
156	Sonbhadra	Ghorawal	1	2	2	No issue
157	Sonbhadra	Pipri	2	4	4	No issue
158	Sonbhadra	Renukoot	4	8	8	No issue
159	Unnao	Mohan	2	1	1	No issue
160	Unnao	Nyotani	2	1	1	No issue
161	Varanasi	Gangapur	2	2	1.65	No issue
Total			868	1456.58	1344.07	

Annexure-6.4

Solid Waste Progeess Report					
Current Status					
2 WTE Plants					
S.no.	Name of the Unit	Address	Waste Disposal Capacity (TPD)	Status(Operational/N on-Operatinal)	Issues related to progress
1	ROLLZ INDIA WASTE MANAGEMENT PVT LTD ,	293M, Village Deenanathpur Puthi, Dasna, Ghaziabad (WTE)	73.97	Operational	
2	K. K. Duplex and Paper Mills	Muzaffarnaggar	120	Operational	
Total Capacity			193.97		



Current Status of SWM

Under Construction Plant(7526 TPD)

Total Plants	Timeline	Capacity	100% Work Completed Sites	70% to below 100% Work Completed Sites	30% to Below 70% Work Completed Sites	Below 30% Work Completed sites
<u>36 Plants</u>	June-2023	4305	<u>16</u>	<u>12</u>	<u>5</u>	<u>3</u>
<u>94 MRFs</u>	March-2023	470	<u>9</u>	<u>50</u>	<u>19</u>	<u>16</u>
<u>343 MRFs</u>	Dec-2023	1715	<u>7</u>	<u>11</u>	<u>29</u>	<u>296</u>
Wet waste processing by compost pit(226 ULBs)	Dec-2023	1036	As Previous Status(No Change)			



Timeline
Maybe
Exceeding



Status of SWM

Future Plan (6280 TPD)

Plants Under construction to be made operational by Dec, 2024	11 Plants with 695 TP D capacity (Sambhal, Badaun, Mirzapur, & Fatehpur, Amroha, PDDU Nagar, Shikohabad, Bharwari, Manjhanpur , Bela Pratapgarh and Sitapur). DPR has been prepared for all these projects.
New plants proposed and to be completed and made functional by Dec ,2024	08 Segregated waste plants (Dry waste cum Composting) with capacity 485 TPD (Mahoba, Akbarpur , Hata ,Deoband,Basti,Dadri,Gonda and Hapur) DPR Under Preparation
Waste to energy plants proposed to be made functional by March, 2025	• 5 Bio-CNG plants (Prayagraj, Ghaziabad, Gorakhpur,GB Nagar(Noida+ Greater Noida) and Lucknow) of 1300 TPD capacity. Agreement done with Ever enviro , Land allocated by Nagar Nigam. • 3 Waste to electricity(Ghaziabad, Agra and Muzaffarnagar) of 3,800 TPD capacity. MOU of UDD with GC international.

75 Legacy waste site Status									Annexure-9	
S. No.	District	Ulb Name	Dumpsit e Area	Remediated land	Waste Quantity (Ton)	Waste Remedia ted(Ton)	Funded By	Remediation Status	Date of Completion	
1	Pilibhit	Pilibhit (NPP)	10	10	38645	38645	By SBM U	Work Completed		
2	Unnao	Unnao (NPP)	6	5.783880372	42532	42532	By SBM U	Work Completed		
3	Fatehpur	Fatehpur (NPP)	7	6.999150589	41205	41205	By SBM U	Work Completed		
4	Mirzapur	Mirzapur (NPP)	12	12	8803	8803	By SBM U	Work Completed		
5	Amroha	Amroha (NPP)	6	5.22	49061	44850	By SBM U	Work Commenced	Mar-23	
6	Hapur	Hapur (NPP)	3	2.52	85171	71543.64	By SBM U	Work Commenced	Apr-23	
7	Hathras	Hathras (NPP)	10	9.2	77184	77184	By SBM U	Work Completed		
8	Mainpuri	Mainpuri (NPP)	4	3.48	173342	173342	By SBM U	Work Completed		
9	Etah	Etah (NPP)	2.6	2.6	88725	88725	By SBM U	Work Completed		
10	Raebareilly	Raebareilly (NPP)	29.4	29.4	62770	62770	By SBM U	Work Completed		
11	Rampur	Rampur (NPP)	22.15	9.303	163823	60000	By SBM U	Work Commenced	Sep-23	
12	Muzzafarnagar	Muzzafarnagar (NPP)	14.5	4.35	224655	67396.5	By SBM U	Work Commenced	Oct-23	
13	Etawah	Etawah (NPP)	3	2.7	81314	81314	By SBM U	Work Completed		
14	Lalitpur	Lalitpur (NPP)	2.5	0.676485369	51738	14000	By SBM U	Work Commenced	Dec-23	
15	Badaun	Badaun (NPP)	1	0.5	46246	46246	By SBM U	Work Completed		
16	Kannauj	Kannauj (NPP)	2.6	1.3	33384.5	18361	By SBM U	Work Commenced	Jun-23	
17	Sambhal	Sambhal (NPP)	7.37	0.3685	49061	2453.05	By SBM U	Work Commenced	Jun-23	
18	Ballia	Ballia (NPP)	5.62	0	337714	0	By SBM U	Work Commenced	Dec-23	
19	Bahraich	Bahraich (NPP)	1	0.47	30139	30139	By SBM U	Work Completed		
20	Sitapur	Sitapur (NPP)	11.96	0	20882	0	By SBM U	Work Commenced	Dec-23	
21	Firozabad	Firozabad (M. Corp.)	6.2	4.297781977	213794	165000	By SBM U	Work Commenced	Jun-23	
22	Jhansi	Jhansi (M. Corp.)	3.29	2.4675	325000	260000	By SBM U	Work Commenced	Jun-23	
23	Agra	Agra (M. Corp.)	72	72	940000	940000	By ULB	Work Completed		
24	Ambedkar Nagar	Akbarpur (NPP)	8	0	40887	0	By SBM	Work Commenced	Dec-23	
25	Aligarh	Aligarh (M. Corp.)	15	0	131424	0	By ULB	Work Commenced	Dec-23	
26	Ayodhya	Ayodhya (M. Corp)	22	20.9	77760	73872	By ULB	Work Commenced	Dec-23	
27	Azamgarh	Azamgarh (NPP)	5		25603	0		CSWAP	Mar-24	
28	Banda	Banda (NPP)	3.46		16425	0			Mar-24	
29	Bagpat	Baraut (NPP)	3.26	3.26	12000	12000		Work Completed		
30	Bareilly	Bareilly (M. Corp.)	23	18.4	406975	250000	By ULB	Work Commenced	Dec-23	
31	Basti	Basti (NPP)	4.2	0.42	20000	2000		Work commenced	Jun-23	
32	Bulandshahar	Bulandshahar (NPP)	5	1	10000	4000	By ULB	Work Commenced	Mar-24	
33	Sambhal	Chandausi (NPP)	4.96	0	29328	0	By SBM	Work Commenced	Mar-24	
34	Ghaziabad	Ghaziabad (M. Corp.)	32	32	400000	400000	By ULB	Work Completed		
35	Ghazipur	Ghazipur (NPP)	1.48	1.48	4500	4500	By ULB	Work Completed		
36	Jaunpur	Jaunpur (NPP)	3.6	0	31025	0		Work Commenced	Mar-24	
37	Kanpur	Kanpur (M. Corp.)	61	32.19444444	900000	525000	By ULB	Work Commenced	Mar-24	
38	Loni	Loni (NPP)	1.89	1.512	72000	60000	By ULB	Work Commenced	Dec-23	
39	Lucknow	Lucknow (M. Corp.)	24	22.8	650000	617500	By ULB	Work Commenced	Jun-23	
40	Mathura - Vrindavan	Mathura -Vrindavan (M. Corp.)	9	1.8	260000	55000	By ULB	Work Commenced	Dec-23	
41	Mau	Maunath Bhanjan (NPP)	2		5000	0		Work Commenced	Mar-24	
42	Meerut	Meerut (M. Corp.)	8	8	300000	300000	By ULB	Work Completed		
43	Ghaziabad	Modinagar (NPP)	2	0.2	10000	3000		Work commenced	Dec-23	

[illegible]
